# Depot Park Update


Gainesville City Commission November 13, 2006

# Park Concept Created 2002 by Genesis Group Accepted by City Commission February 24, 2003 Historic Depot Trail Depot Building Parking Waterside Promenade Amphitheater Play Area Trails – walking and biking Boardwalks Botanical Garden

### Park Benefits

Manage and treat storm water


Provide recreation area
Support redevelopment
Attract and retain residents
downtown





# Phase 1 Development (Funded)

Groundbreaking 2/05
West ponds finished 4/06
Plantings

Landscaping/trails



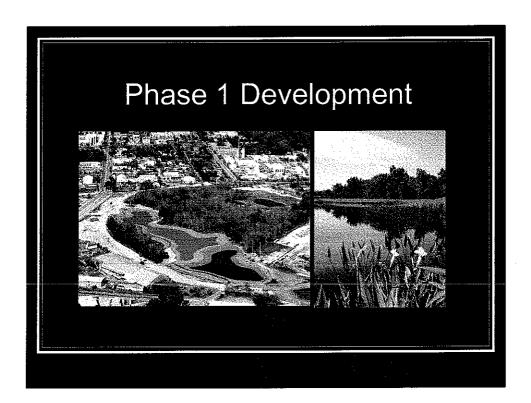

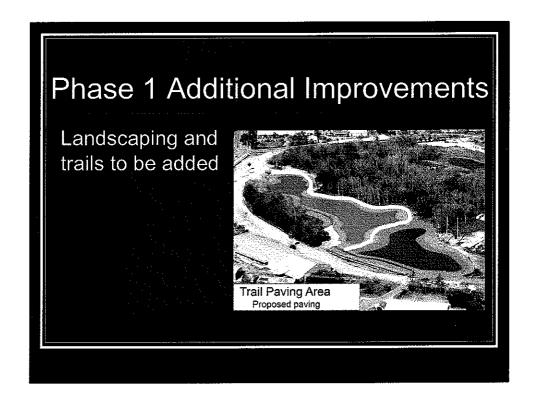

### Phase 2 Development (Funded)

Phase 2 to start early 2008

Coal tar remediation

East pond


Stormwater system

**Pond Plantings** 

Amphitheater grades

Funded by GRU and

Stormwater Management Utility



### Phase 3 Recreation Elements

FUNDED \$700,000

Depot Park Trail

PARTIALLY FUNDED \$1.9 M

Historic Depot Trail \$2.8 M

Parking Facilities \$520,000

UN-FUNDED \$4.9 M

Promenade \$475,000

Amphitheater \$2.0 M possible


Childrens' Play Area \$130,000

Woodland Trail \$700,000

Wetland Trail \$860,000

Botanical Garden Center \$750,000

possible



### Existing Funding for Recreation

UDAG: \$1,253,600 to be rec'd by end of 2013

Cap. Improvement Bonds: \$1,000,000

Recreational Trail Program grant: \$200,000

HUD EDI grant: \$148,800 Total funding = \$2,602,400


### Future Recreation Funding

### Gift Catalog

### Grants

- FL Recreation Development Assistance Program
- HUD Economic Development Initiative
- Recreational Trails Program
- · Cultural Facilities Grant



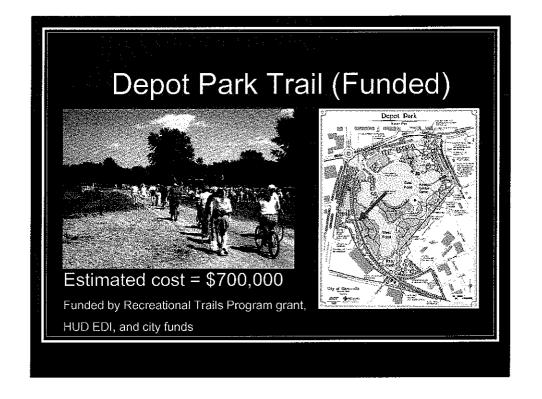

### **Depot Building**

Historical context proposal accepted by SHPO

Usage to be determined Area = 10,000 square feet




## Amphitheater

Initial grading part of Phase 2 construction plans


Showmobile as interim stage

Future stage to be fixed base


Capacity for 3000 possible






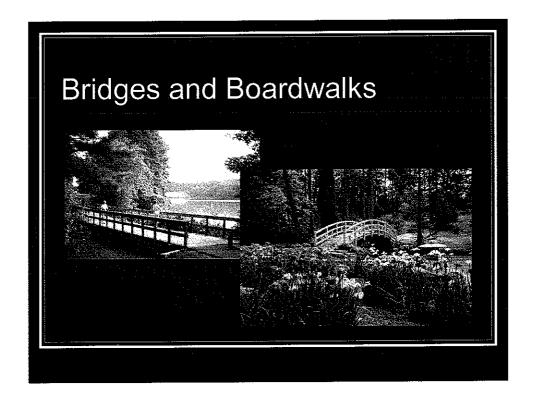



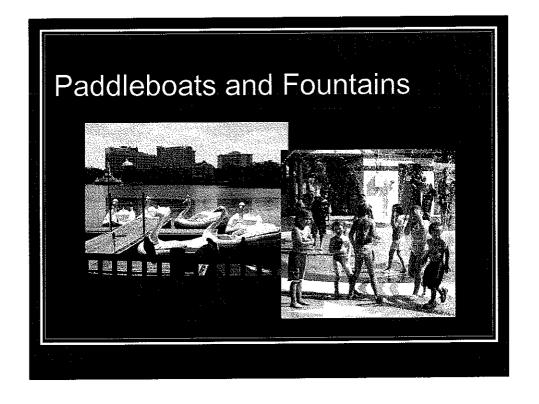

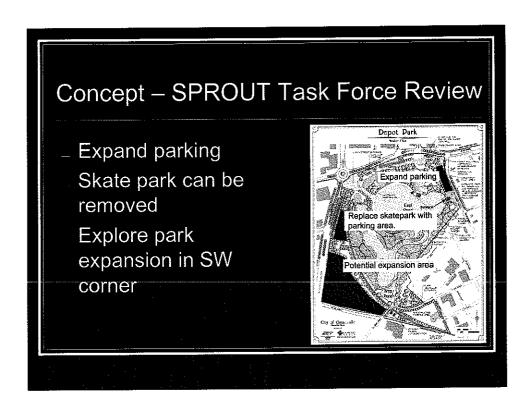



### Park Development Timeline

- Phase 1 landscaping and trails 2007
- Depot Park Trail 2007
- Phase 2 pond finish mid-2009
- Phase 3 park construction start mid-2009

### Recommendations

- Move forward on concept with changes
  - · Remove skatepark and expand parking
  - · Consider expansion on southwest corner

Finish Phase I work in 2007

Initiate discussion on Depot building uses for planning rehabilitation
