



Legislative ID #080479B

Project Update: DEPOT AVENUE TRANSPORTATION CORRIDOR


SW 13TH ST (US 441) TO SE 11TH ST (WILLISTON ROAD)

Presented by
City of Gainesville Public Works Department
to the
Metropolitan Transportation Planning Organization
August 23, 2010

Project Description

- The project is to provide for reconstruction of Depot Avenue from SW 13th St to Williston Road to an urban roadway, including roundabouts, pedestrian and bicycle facilities, decorative lighting, streetscape and landscape amenities.
- The corridor has been divided into 4 separate segments to accommodate the different roadway lane configurations.

Roadway Segments

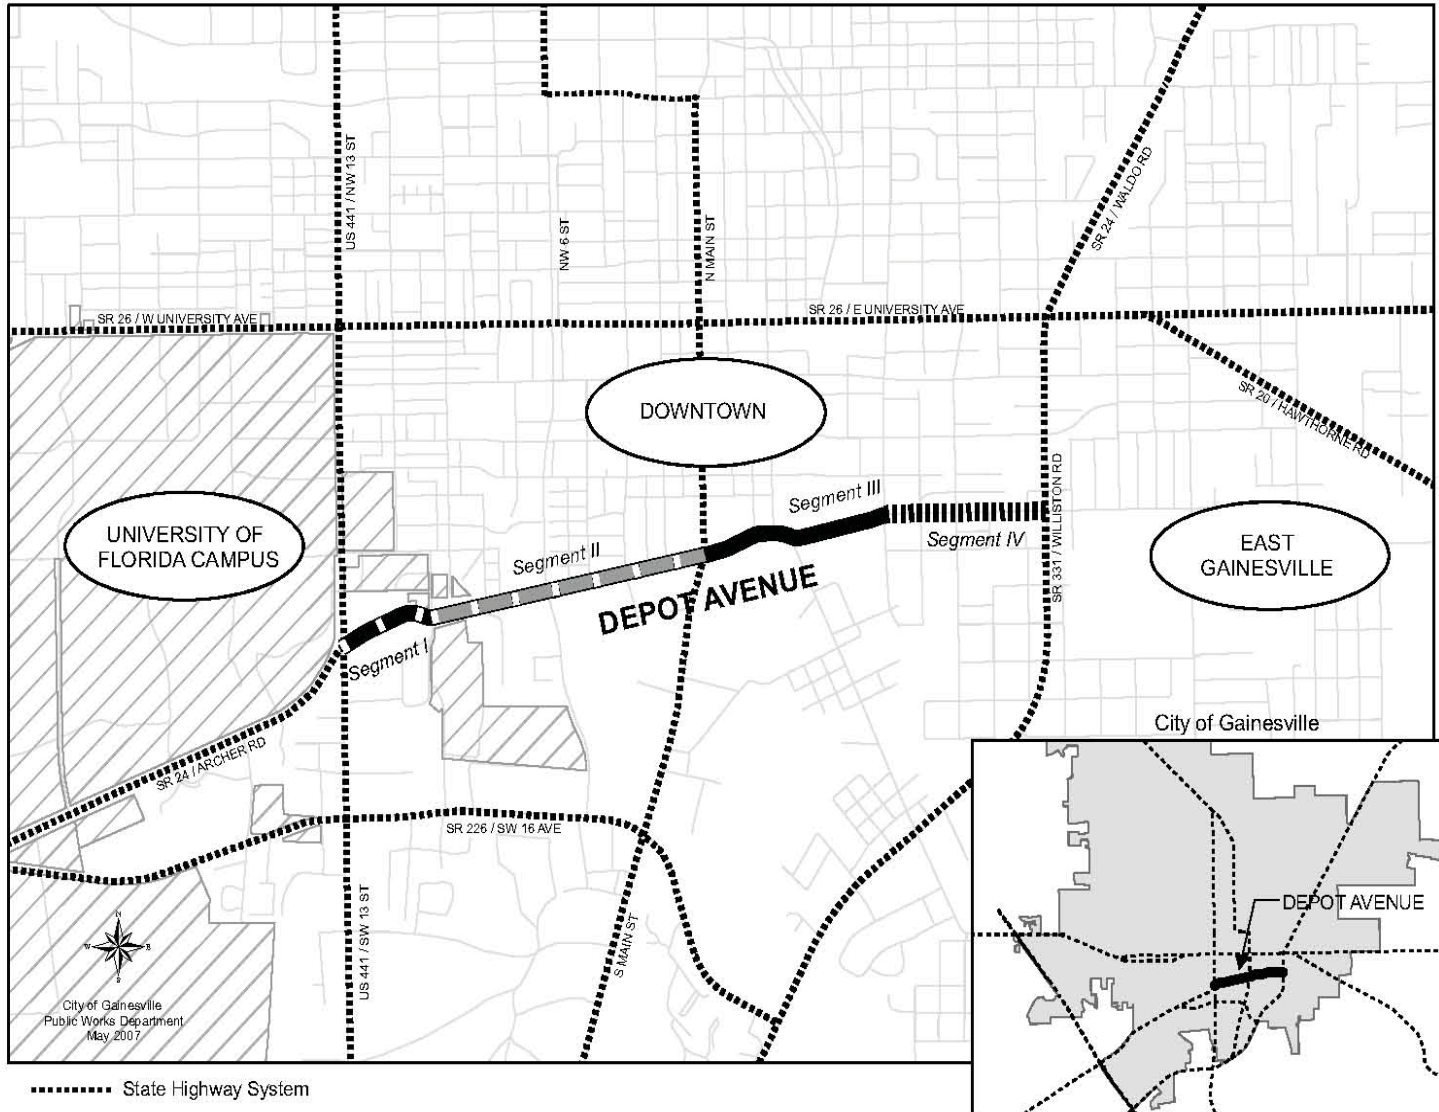

Proposed Improvements

- Completed corridor study in 2003: identified multiple lane alternatives for each of the 4 segments
 - Segment 1: Milling and Resurfacing
 - Segment 2: Reconstruction, including roundabouts at SW 11th St, SW 6th St, and Main St
 - Segment 3: Reconstruction, including a roundabout at SE 4th St
 - Segment 4: Reconstruction, including a roundabout at SE 7th St

Project Status

Segment 1

- Not Begun

Segment 2

- Design: Underway (90%, est. completion- Dec. '10)
- ROW Acquisition: Underway (completion Mar '12)

Segment 3

- Design: Completed
- Construction: Underway (completion- Nov. '10)

Segment 4

- PD&E: Completed 2007
- Design: Underway (30%, est. completion- June '11)
- ROW Acquisition: Underway (complete Mar '12)

Cost Estimates

Phases Underway (\$7.4M):

Segment 2: Design (\$1.0M); ROW (\$3.8M)

Segment 3: Construction (\$1.3M)

Segment 4: Design (\$0.4M); ROW (\$0.9M)

Future Phases (\$4.7M):

Segment 1: Design/Construction (\$0.3M)

Segment 2: Construction (\$3.2M)

Segment 4: Construction (\$1.2M)

Total: \$12.1M * based on latest contract prices

Available Funds:

- Federal Earmarks: \$4.2M
- Local Funds (LOGT & Other): \$4.8M
- County Incentive Grant: \$3.8M (programmed for FY 12)
- HUD-EDI: \$0.2M

Total: \$13.0M

Project View

BEFORE

Segment 3: Intersection
of Depot Avenue &
SE 4th Street



Eastbound Approach



Northbound Approach



Project View

AFTER

Segment 3: Intersection
of Depot Avenue &
SE 4th Street



Eastbound Approach



Northbound Approach

