

A.QUINN JONES MUSEUM



Community Redevelopment Advisory Board April 18, 2016





- Construction Update
- Next Steps
- City Partnership
- Projected Opening



Construction Update

- Phase I Interior Build-out
 - At substantial completion
 - Certificate of Completion
- Phase II Site Work & Landscaping
 - Projected to start by mid-May with target completion of late summer
 - Certificate of Occupancy



Construction Photos

A.QUINN JONES MUSEUM




















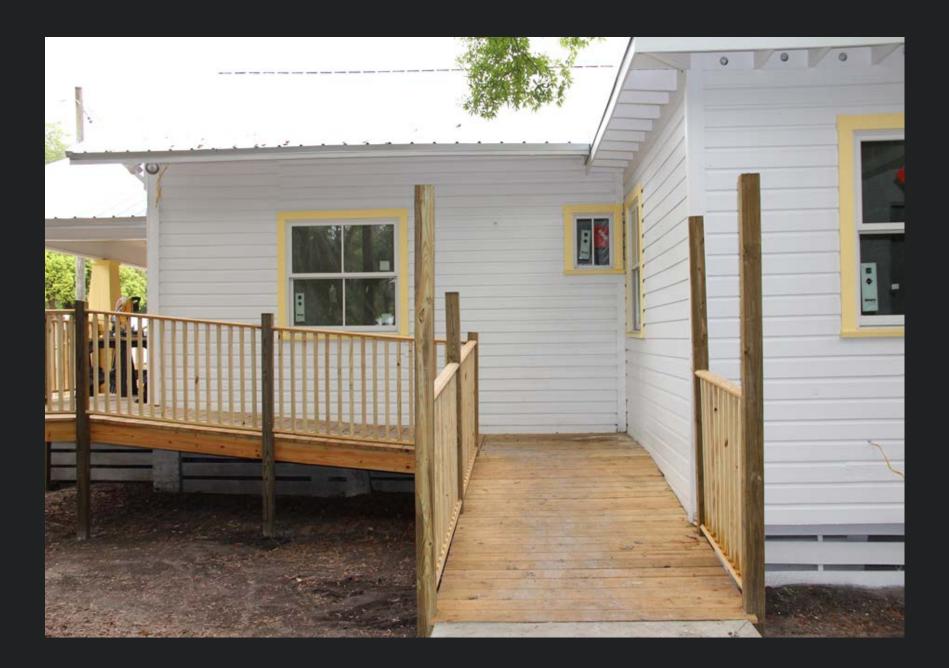







Next Steps

- User Interviews
 - Identify what user groups want/need
 - School board, State Heritage Trail, etc.
 - One-on-one, group, Survey Monkey, etc.
- Exhibit Design
 - Fixed AQJ exhibit
 - History/Civil Rights
 - Specific focus on education





City Partnership w/ PRCA

- Desire for AQJ to be managed by PRCA
- Collaboration on Exhibit Design
- Augment Fundraising & Programming



GAINE VILLE



Putting AQJ & Gainesville "on the map"





Ribbon Cutting GOAL = February 2017 Black History Month



Hear Presentation from Staff
