

# LEGISLATIVE # 110264C





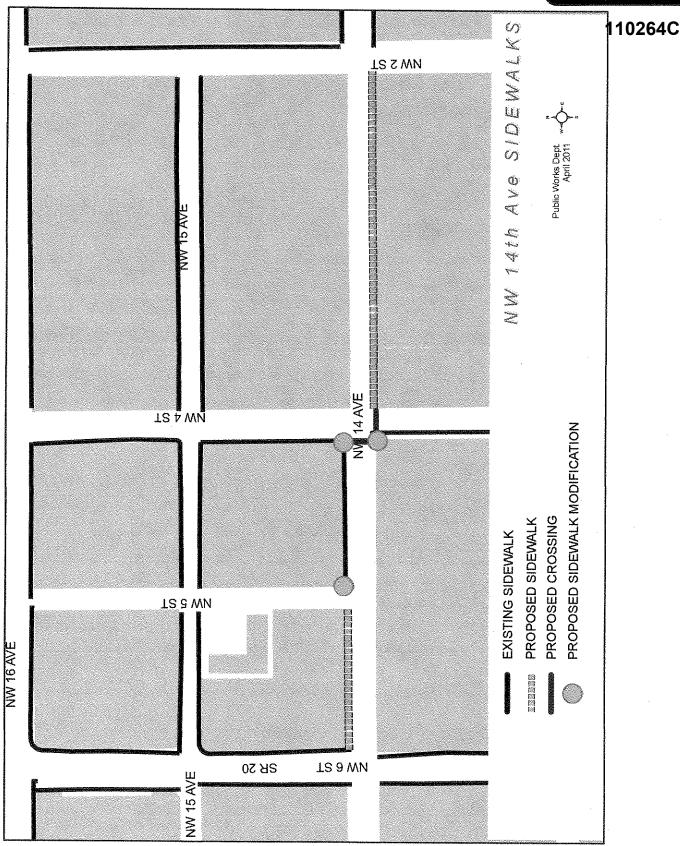

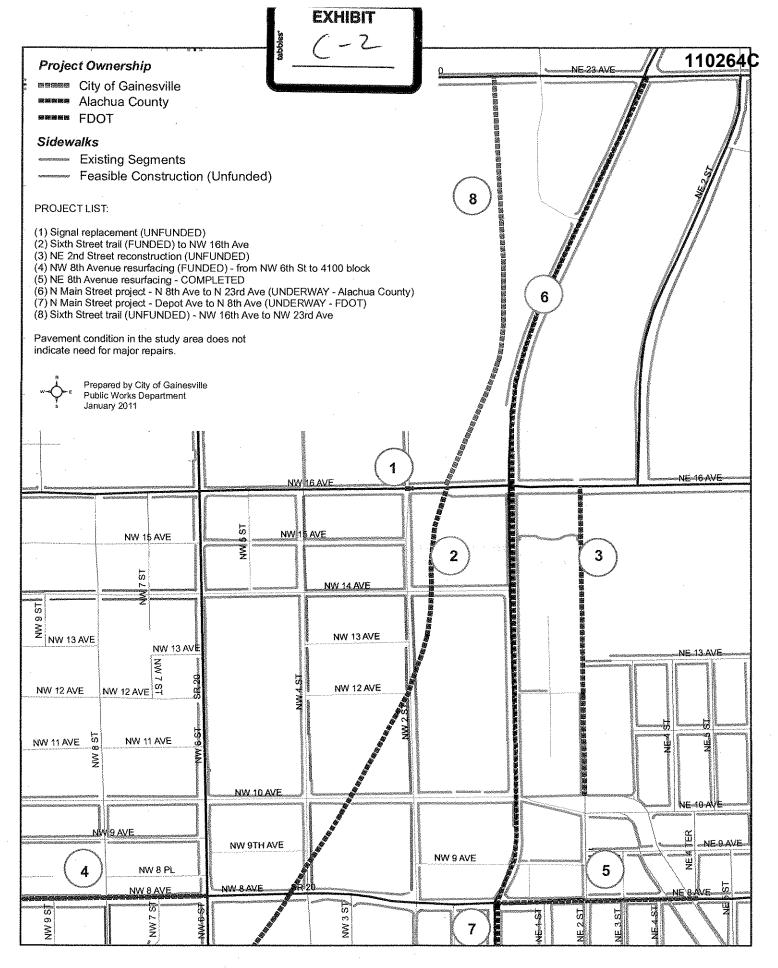

**Alachua County Public Works Department Engineering and Operations Division** 

# Project No. 6336 Main Street Mill and Resurface

Contract Details

Contractor-

APAC-Southeast,

Inc.

Contract Amount- \$1,179,041,31

% Complete—

(Design 100%) Construction—0%

### Project Schedule

Bid Revised— Award Revised— February 2011 NTP Revised— June 2011 Final Comp.—

September 2010 December 2011

### Project Description

- MIII and Resurface of Main Street from north of NW 8th Avenue to NW 23rd Avenue
- Restripe from north of 8th Avenue to NW 16th Avenue to a 3 Lane cross section to match FDOT project.
- Construct a mid-block crossing and medians
- Widen sidewalk on the east side to 8' for multi-use path
- Fill in missing sidewalk sections on the west side if easements are obtained.
- **Construct Mast Arms and** Signal upgrades at 10th and 16th.
- Project funded by Gas Tax.

### **Construction Team**


Design: Gaelan Bishop, PE, Volkert & Associates

PM: Chris Zeigler. ACPW

## **Project Progress**

**EXHIBIT** 

- A Public Information Meeting was held on 1/12/09.
- FDOT has identified stimulus money for the milling and resurfacing portion of the project
- The Tire Outlet agreed to right-in/right-out for northern driveway.
- FDOT completed mill and resurface from NW 8th Avenue to NW 23rd Avenue 3 months ahead of schedule.
- ACPW revising plans to remove work done by FDOT
- ACPW is coordinating with the City of Gainesville arborist to develop a mitigation plan for the trees that were removed. Working with No-Fault Car Insurance, Post Office, and Auto-mall to obtain TCE"s and sidewalk easements.
- Received easements from U-haul, Gainesville Shopping Center, Celebrations, Tires Plus, Popeyes, Midas, Chevron and Burger King
- Bid opened on December 15, 2010
- Lowest apparent bidder was APAC at \$1.2 million.
- BoCC approved awarding bid to APAC-Southeast on February 8th, 2011.
- Contract Aaward by BoCC on March 22nd.
- Pre-construction meeting held on May 17th.
- Noticie to Proceed issued for June 20, 2011
- Contract Time is 180 days
- Construction time began on June 20, 2011.
- Preparing change orders to remove driveway work at Tire Outlet and to repair cracked inlet top.
- Finished installation of four drilled shafts for signal reconstruction.
- The contractor is reconstructing driveways and sidewalk on the west side of the road.
- Preparing change orders to reconstruct U-haul and Tires Plus driveway.

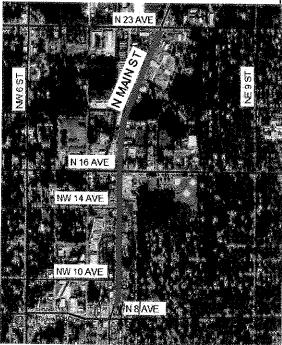

Last Updated: Monday, August 01, 2011
