Depot Park Update and Development Action Plan




March 17, 2008 Gainesville CRA



Vision

- The vision for Depot Park is to create a contemporary public greenspace that will serve as Gainesville's "Central Park."
- As the signature city park located within downtown, it will be the gateway to central Gainesville and provide a space for public outdoor enjoyment unique to the city.

Depot Park Area Coordination

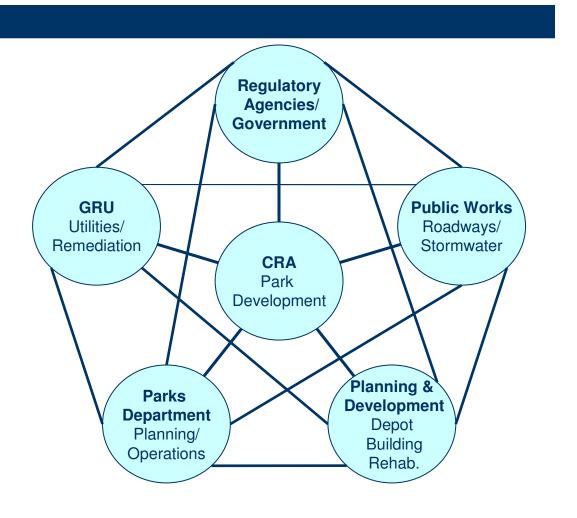

Remediation

- Conceptual approval given to remediate the coal tar contamination with treating soil from the Poole Roofing and Depot Park sites (Poole/CSXT IRA and former-CSX site respectively) followed by groundwater monitoring.
- Remediation of Phase 1 (Poole Roofing) to start September 2008, followed by Phase 2 (Park Site) in January 2009.

Schedule Acceleration

- Aggressive steps are being taken to meet the cleanup target date of late 2009 and accelerate park construction.
- Additional funding is needed on an accelerated schedule.

Park Construction Schedule

- A portion of the park site is now available for landscape improvements, but stormwater and park elements cannot start before the end of remediation in December 2009.
- Funded park projects can enter the design stage as early as mid-2008 with a construction start goal in late-2009 – early 2010.

Projects with Funding	Start	End	Cost
Rinker Building Demo	Apr-08	May-08	\$12,000
Depot Ave Phase I	Oct-08	Oct-09	\$2,500,000
Remediation Phase I	Sep-08	Dec-08	\$5,000,000
Remediation Phase II	Jan-09	Dec-09	\$9,000,000
Stormwater Pond	Jan-10	Dec-10	\$4,000,000
Design & Tech Standards	Mar-08	Jul-08	\$49,000
Depot Building Rehab Plans	May-08	Jul-08	\$25,000
Depot Building Move	Jul-08	Jul-09	\$100,000
Landscape Phase I	Sep-08	Nov-08	\$200,000
Design - Depot Park Trail	Aug-08	Jan-09	\$70,000
Design - Historic Depot Plaza	Jan-09	Jul-09	\$120,000
Design - North Pond Promenade	Jan-09	Jul-09	\$50,000
Design - General Improvements	Jan-09	Jul-09	\$200,000
Design - Phase II Landscaping	Jan-09	Jul-09	\$40,000
Construct - Depot Park Trail	Jan-10	Jun-10	\$630,000
	Total Project F	\$21,996,000	

Graphic
Timeline of
Park
Development




Carol Johnson and Associates is creating Design and Technical Standards

Beginning point for all project design



GRU is installing utilities up to boundaries of remediation


Completes in early 2009 after remediation in this area concludes

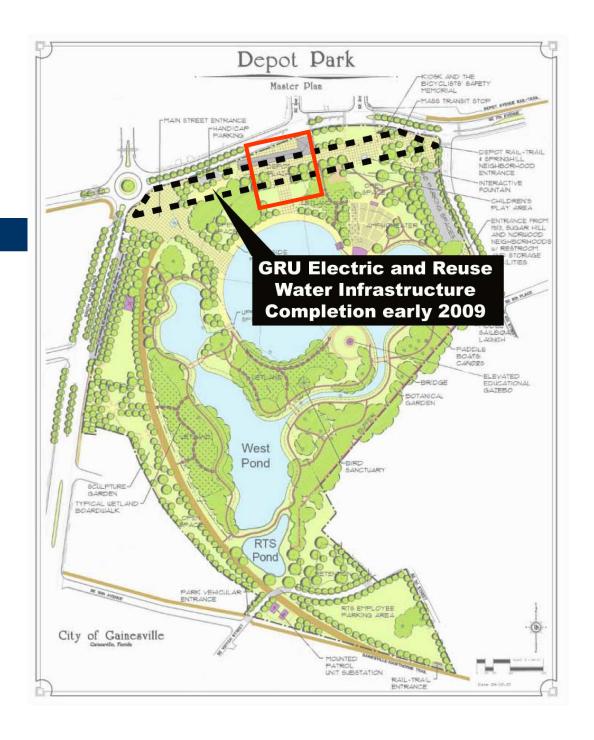

Cade Museum Charrette

Demolish former-Rinker building

FDEP completes assessment on dry-cleaning solvents in May

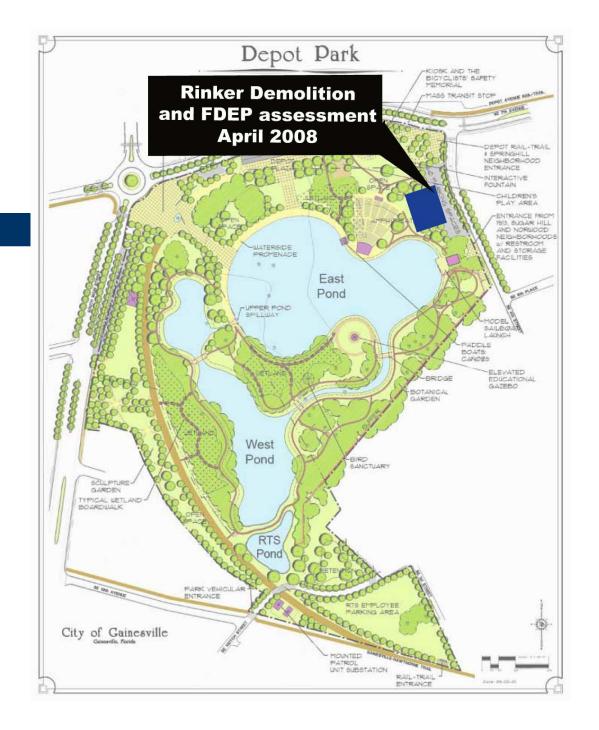


Mid 2008

Phase 1 landscape installation to begin




Mid 2008

FDEP approvals may be obtained for moving the building to facilitate cleanup

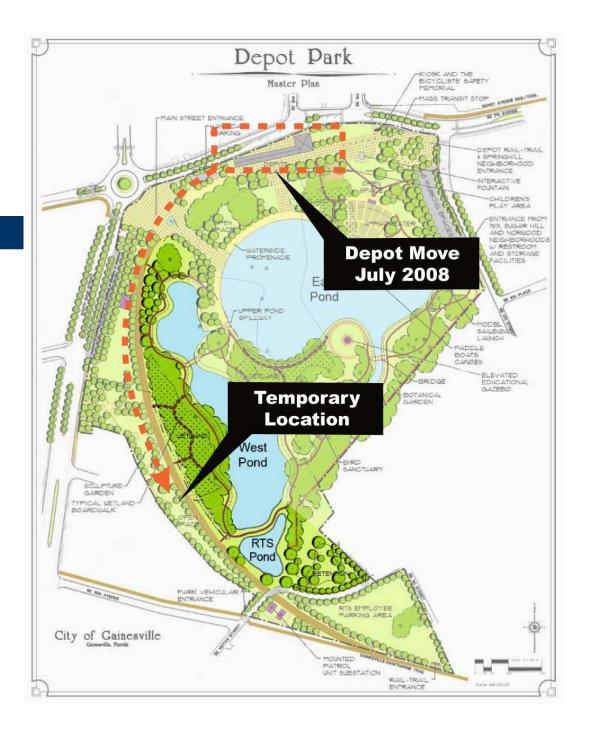

Mid/Late 2008

Depot is secured and rehabilitation can begin

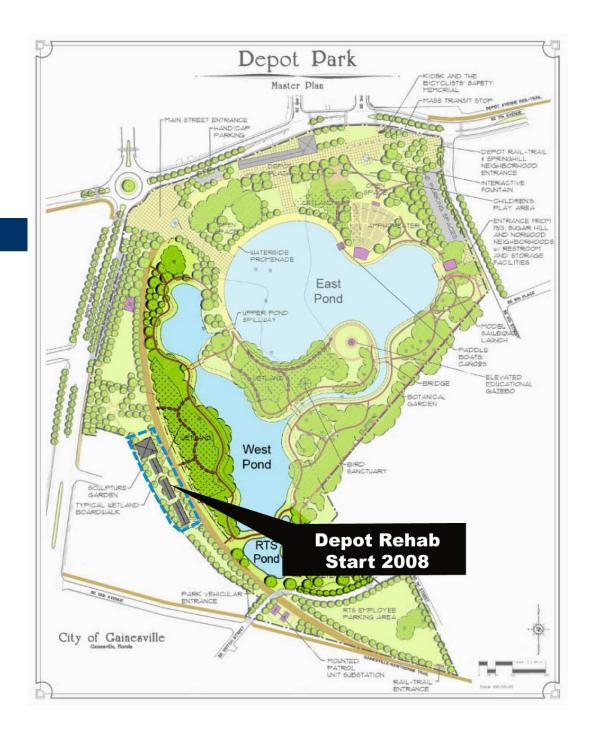


The site will be controlled and closed off to general access

Depot Avenue will be closed in the construction zone



Begin Phase 1 Poole Roofing/CSX IRA

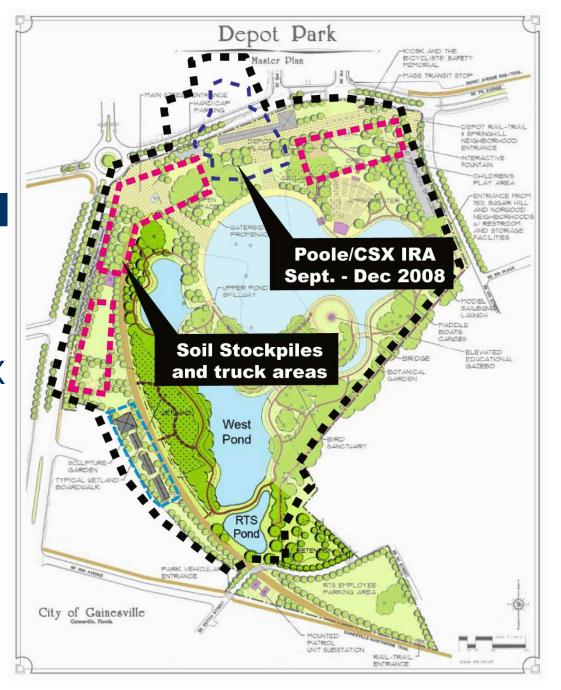


Cleanup in progress

Begin Depot Avenue Reconstruction Phase 1




Phase 1 is finished

Depot moves back to permanent site, rehab continues

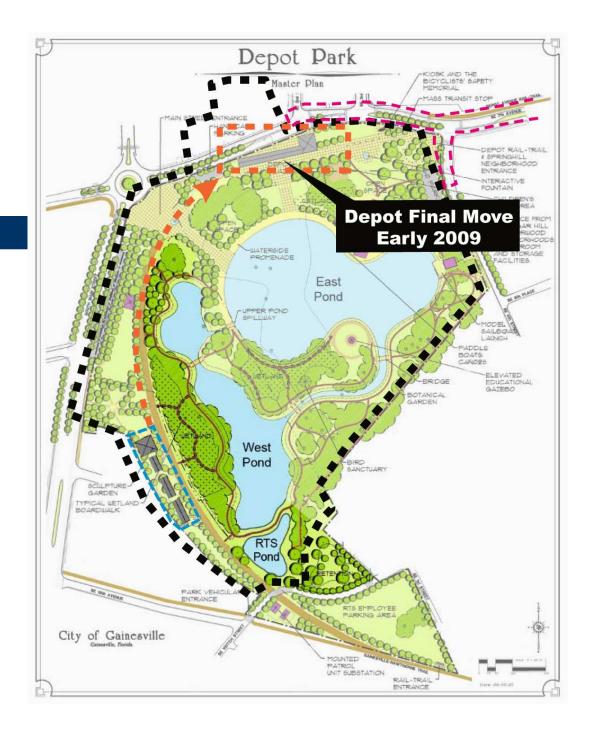


Begin Phase 2 park cleanup on former-CSX site

Depot Avenue Phase 1 inprogress and will end in late 2009

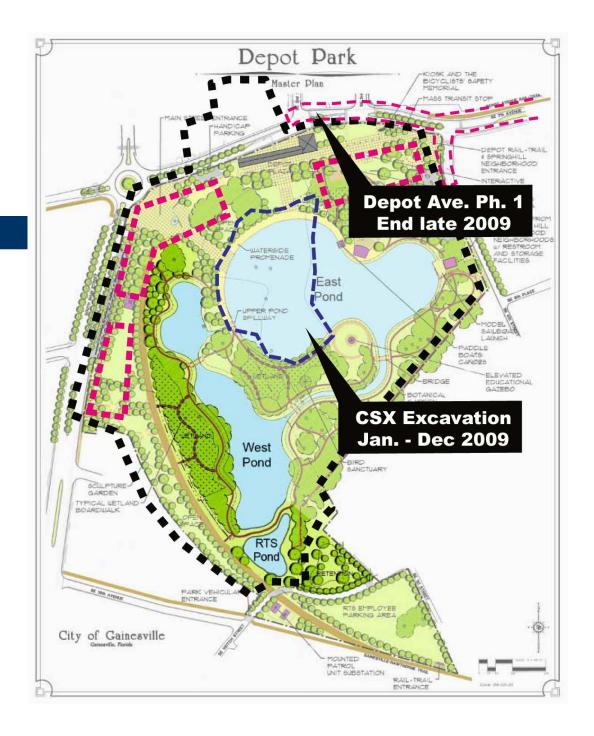

Project Budget

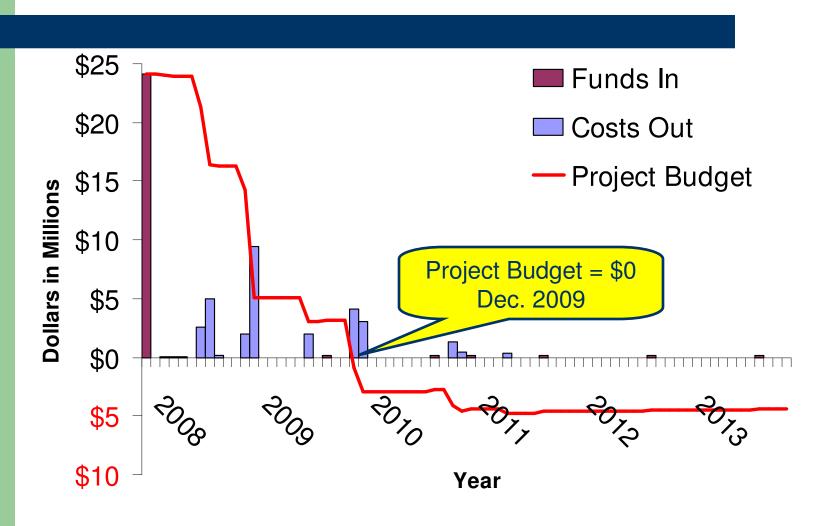


Unfunded Projects

Project	Cost	Start	End	Funding Gap
Depot Ave Phase II	\$2,000,000	Oct-09	Apr-10	\$1,000,000
Depot Building Rehab	\$2,000,000	Jul-08	Aug-09	\$500,000
Construct - Historic Depot Plaza	\$1,800,000	Apr-10	Sep-10	\$1,800,000
Construct - North Pond Promenade	\$450,000	Aug-10	Jan-11	\$450,000
Construct - General Improvements	\$1,325,000	Apr-10	Sep-10	\$1,325,000
Construct - Phase II Landscaping	\$360,000	Jan-11	Jul-11	\$360,000

Total Funding Need = \$5,435,000

Depot Avenue Phase 2 starts in October

Cleanup ends in December pending FDEP approval

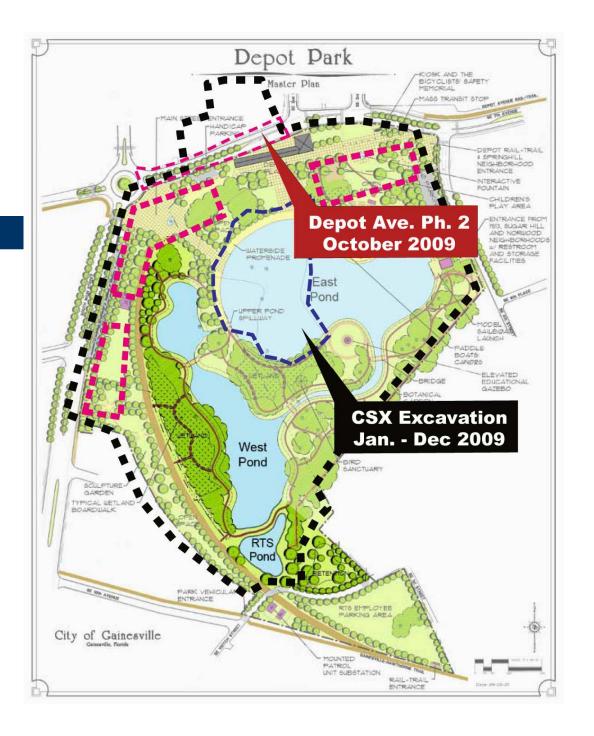

Depot Avenue Phase 2 ends

East Pond is under construction



Early/Mid 2010


Depot rehab concludes

Construct Depot Plaza & Trail and Depot Park Trail



East Pond construction ends

Begin construction of Pond Promenade

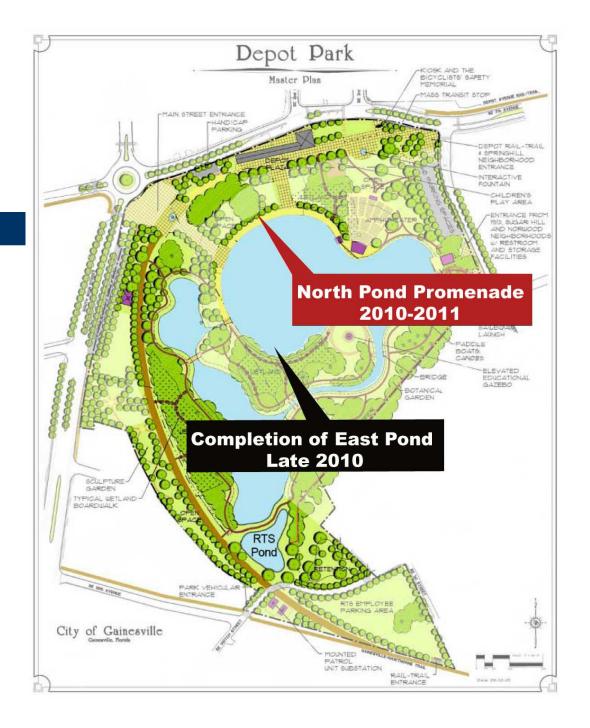

Start construction of entrances, parking, walkways and landscaping



Park is essentially complete



Recommendations

- 1. CRA request the City Commission to designate the CRA as the lead agency for the construction of the park and recreation elements on the site and for the depot building rehabilitation and authorize the CRA to assume leadership of the Depot Park Team, to be comprised of CRA, GRU, Public Works and Parks, Recreation and Cultural Affairs staff.
- 2. CRA refer the selected project acceleration strategy (maintain flexibility to use the "City's Best Interest" procurement) to the City Commission for approval and authorize staff to modify the project documents accordingly.
- 3. CRA request that the City Commission address the approximately \$4 million capital funding gap for park and recreation improvements.

Recommendations

- 4. CRA request that the City Commission establish late-2009 as the target completion date for remediation and start date for constructing the remaining park and recreation improvements.
- 5. CRA request that the City Commission direct Public Works Stormwater Management Utility fund landscape improvements in and around the stormwater ponds instead of using park development funds.
- 6. CRA request that the City Commission direct Public Works to secure adequate funding to start the Phase 2 reconstruction of Depot Avenue between South Main Street and SE 2nd Street by late-2009 and to determine funding needs to address arsenic remediation on the park site.

Recommendations

- 7. CRA request that the City Commission address the approximately \$500,000 funding gap for restoring the Depot Building and authorize staff to pursue beginning the rehabilitation while the building is in storage in 2008.
- 8. CRA request that the City Commission accelerate funding of park projects by making funds equal to the remaining UDAG grant proceeds (total of \$809,879) available in fiscal year 2009 instead of 2013.
- 9. CRA authorize staff to provide updates on Depot Park project milestones on a bi-monthly basis.
