### ${\it J.E. Decker Construction Group\ CONSTRUCTION\ CHANGE\ ORDER\ PROPOSAL}$

Date:	April 1, 2020		4
Architect/Engineer	Jay Reeves & Associates, Inc.	Change No:	4
To (Contractor):	J.E. Decker Construction Group	Project:	Historic Hartman House at Hogtown Creek Headwaters
Address:	PO Box 358973, Gainesville, FL 32635	Purchase Order	PD 850 85100620190073
		A/E Job No:	TBD

### YOUR PROPOSAL HAS BEEN ACCEPTED FOR MAKING THE FOLLOWING CHANGES:

		PROPOS	ED CHANGE		CM	ODP Tax	Bid Package	Construction	n Contract
No.	Description				Contingency	Savings	Savings	DECREASE	INCREASE
	A. Bid package s		nd buyout to date				<b>AT</b>		
	07A New Roof - \$						\$5,898.00		
	09A GWB Assem						(\$1,285.00)		
	09C Flooring - \$1 10A Specialties (I		\ \$1,000				\$895.00 TBD		
	23A Mechanical/F						\$303.00		
	26A/28A Electrica						\$303.00 TBD		
-	ZUA/ZUA LIECTICA	aι - ψ29,500	,				TOO		
	B Provide and i	nstall new	siding due to co	ondition of existing siding	after demolition	started Existing	siding was		
-				rpentry work to restore b	•				
-				Also the discovery of the					
				insulate the walls which					
				t page stating that "the					
				nd bevond ROUGH & FIN					
	07 Siding Materia	l allowance	is to be above an	ia bevona Rough & Fin	SH CARPENIKI	nat was included	in the GiviP.		\$5,585.00
	07 Siding Labor a								\$5,835.00
-									<del>\$0,000.00</del>
-	C. Provide and	install add	litional window t	rim and interior trim wor	k. Original GMP o	lid not include fun	ds to rebuild		
				be reused. Field determ					
				ng windows. New window					
				I GMP did not include fu					
				ot been included in origi					
				is to be above and beyon					
	in the GMP.	ization. w	re understand th	is to be above and beyon	a ROUGH & FINIS	n CARPENIKI III	at was included		
	06 Carpentry Mat	erial and I	ahor allowance						\$7,020.00
-	00 Carpentry Wat	Criai and L	abor allowarioc						Ψ1,020.00
-	D. Bid Package	Savings II	sanes						
-				iding change order			(\$5,811.00)		(\$5,811.00)
-	Otilize bia paeriag	o oavingo	to partially cover c	iding change craci			(ψο,στι.σσ)		(ψυ,υ11.00)
-	E. User Group d	riven char	nges						
-				Requested upgraded applia	nces				\$948.00
-	26/27 Added rece			toquootou apgradou applic	11000				\$1,850.00
	20/21 /100001000	practice an	a data rough in						Ψ1,000.00
-	F. Staffing / gene	eral condi	tions for change	s to date					
-				g and trim carpentry					\$8,120.13
	changes above a			g and ann carponal					\$0,120.10
				litional 4 weeks (1 month)					\$850.00
-				n beyond original scope.					Ψ000.00
-				for an additional 4 weeks	(\$8,120.13)				
				eline) for unforeseen	(\$0,120.10)				
	existing conditions								
-				ent vehicle / equipment for	(\$850.00)				
-	an additional 4 we				(\$000.00)				
-	completion timelin								
	Jon p. Julion union	,							
	G. Door scope o	hange due	e to condition of	existing doors and scope	increase				
				d repair of 3 existing					\$11,276.16
-				loors. Includes value-					<b>\$11,210110</b>
-				nimize additional cost.					
	silgilloolog (VL)	acoro puon	ago in order to mi	Contractual OH&P 15%					\$5,350.99
-				Insurance 2.5%					\$1,025.61
-				Bond 2%					\$841.00
NOTICE	TO PROCEED DATE		6/20/2019	Dona Z/o	(\$8,970.13)	\$0.00	\$0.00	\$0.00	\$42,890.89
	AL CONTRACT SUM		\$399,867.00		(ψ0,370.13)	φυ.υυ	φυ.00	φυ.υυ	Ψ-72,030.03
Contrac	t Time: Contract:	Days	Complete *	Duna	¢17.070.20	\$0.00	\$0.00	Drocont Cum	¢425 214 50
		402	7/26/2020 7/26/2020	Present:	\$17,978.38	\$0.00 \$0.00	\$0.00 \$0.00	Present Sum:	\$435,214.58
This Cha		0		Change:	(\$8,970.13)			Add / (Deduct):	\$42,890.89
New Co	ntract Time:	402	7/26/2020 staffing conditions an	New:	\$9,008.25	\$0.00	\$0.00	New Sum:	\$478,105.47

Final Completion Date. Requested staffing conditions and contract time are contingent on availability of work force, CM's continued access to site pending any action taken by any government entity limiting operations.

### CHANGE ORDER#4 HISTORIC HARTMAN HOUSE AT HOGTOWN CREEK HEADWATERS

### A. BID PACKAGE SAVINGS AND BUYOUT TO DATE 07A – NEW ROOF

07A	NEW ROOF (MAIN HOUSE - METAL)		

WWW.JEDECKERCONSTRUCTION.COM



### **CONCEPTUAL BUDGET**

PROPOSAL BY

J. E. DECKER CONSTRUCTION GROUP, LLC P.O. BOX 358973 GAINESVILLE, FL 32635

	Renovations per plans or as outlined on cover page.	ALLOWANCE	1	\$20,000.00	\$20,000.00
07B	INCH ATION (CELLING 6 MALLS)				

ALLOWANCE \$20,000.00

LESS CONTRACT \$14,102.00

BID PACKAGE SAVINGS: \$ 5,898.00



## **Duffield Home Improvements**

4566 NW 5th Blvd., Suite I Gainesville, FL 32609 Phone 352-375-7008 Fax-352-375-7014

### Lic. #CCC1325785 & #SCC131149785

PROPOSAL SUBMITTED TO:	JE Decker Construction	PHONE:	(352) 318-9149	DATE:	02/17/20
	7 16th Ave	EMAIL:	(882) 818 9119	DITTE.	02/17/20
CITY, STATE and ZIP CODE:	Gainesville FL 32605	JOB LOCATION	Historic Ha	rtman House	/ Gainesville
We hearby submit specification					
5v Crimp Galvalum	e Metal Non-Painted Roofing Pane	el with Expos	ed Fasteners 25 Year l	Manufacture	·V
Install 26 gauge galv	valume over existing dry-in underla	ayment			
Installed with lifetin	ne screws to code				
Install deck tite plun	nbing boots, on ridge ventilation ar	nd ridge cap			
Install new drip edge	e on lower eave area				
Includes 5Yr workm	nanship warranty				
Additional plywood	will be billed @ \$68 per sheet				
Additional dimension	onal wood work will be billed @ \$	5 per ft			\$14,102.00
Alternate:					
Labor only installati	on			per sq	\$275.00
	erials arrive and balance upon completion <b>ibject to manufacturer price inc</b>		<del>-</del>	eyond 30 day	7 <b>S</b>
				Dollars (	\$)
standard practices. Any altera upon written orders, and will b covered by Workman's Comp	d above and installed to specifications in a workmar tion or deviation from above specifications involving become an extra charge over and above the estimated ensation insurance. Owner to carry fire, tornado and rikes, accidents or delays orders beyond our control.	g costs will be exect d price. Our workers d other necessary ins	ated only seare fully urances. All Signature: Illy covered	Blake Note: This pro	York
Florida Statute Section 404.056 "Radon Gas	": Radon gas is a naturally occurring radioactive gas that, when it has accumulat have been found in buildings in Florida. Additional infor				els of radon that exceed Federal and State guidelines
	on Industries Recovery Fund": Payment may be available from the Construction ractor. For information about the recovery fund and filing a claim, contact the Fl				
	Florida Statutes contains important requirements you must follow before you ma ction conditions you allege are defective and provide such person the opportunity offer which may be made. There are strict deadlines a	y to inspect the alleged construc	tion defects and to consider making an offer to rep	air or pay for the alleged cons	
Acceptance of P	roposal The above prices, specifications a	and terms and condi	tions are satisfactory and are here	eby accepted. You	are authorized to do work as
specified. Payment will be ma	de as outlined				
D			Signature:		
Date of Acceptance:			Print Name:		

### A. BID PACKAGE SAVINGS & BUYOUT TO DATE: 09A GWB ASSEMBLIES

From: **Doug Bily** To: Karlin Warkentin

Subject: RE: P385 Hartman House Final Plans approved by City of Gainesville 3-6-20

Wednesday, March 18, 2020 10:14:10 AM Date:

Karlin,

To add the drywall on the walls and ceilings of the Park Office 103 to have an add  $\frac{1}{4}$ f \$1,285.00. Let me know if you have any questions.

Thanks,

### Douglas Bily | Project Manager | Doug@CentralFloridaDrywall.com

Central Florida Drywall & Plastering Inc. | 3307 NE 2nd St, Gainesville, FL 32608

352.376.6606 Direct | 352.538.2512 Cell | 352.372.6606 Fax |

**From:** Lori Brooks <lorib@jedeckerconstruction.com>

**Sent:** Monday, March 9, 2020 10:58 AM

Cc: Karlin Warkentin <karlinw@jedeckerconstruction.com>

**Subject:** P385 Hartman House Final Plans approved by City of Gainesville 3-6-20

Importance: High

Good morning all,

Attached, please find the final approved set of plans for Hartman House. Please use these for the project.

Should you have any questions or comments, please feel free to contact Karlin by phone or email. His contact information is as follows:

Email: <u>karlinw@jedeckerconstruction.com</u>

Cell phone: 352-318-9149

Kind Regards,

Lori Brooks

**Asst. Office Manager** 

### HISTORIC HARTMAN HOUSE AT HOGTOWN CREEK HEADWATERS

### A. BID PACKAGE SAVINGS & BUYOUT SAVINGS 09C - FLOORING

L		Renovations per plans or as outlined on cover page.	ALLOWANCE	1	\$15,000.00	\$15,000.00
	09C	FLOORING (ALLOWANCE FOR NEW and/or REFINISHING)				
		Renovations per plans or as outlined on cover page.	SF	1400	\$10 00	\$14,000.00
Ţ						

ORIGINAL ESTIMATE: \$14,000.00

LESS CONTRACT: \$13,105.00

BID PACKAGE SAVINGS \$ 895.00

### TEAL TILE CARPET ONE

P.O. Box D 131 N. Cherry St. Starke Fl. 32091 Phone (904) 964-7423 Fax (904) 964-9156

To:	JE Deck	er Construction						F	ebruary 3, 2020
	karlinw@	jedeckerconstruction.com							
Attn:	Karlin V	Varkentin							
Job Name:	Historic	Hartman House @ Hog	town Creek						
Scope:		/ Install LVT, Ceramic Ti see attached Finish Pla							
Product:	_		Amtico Spacia I	LVT - 20 mil					
Product:			ris Deluxe 12x2	4 - Floor Tile					
Product:		Iris	s Deluxe 3x12 B	Bullnose - Bas	se .				
Product:			Durock Underla	yment @ FT					
Product:		Schl	luter Reno Ramı	p Tile Transi	ion				
Product:									
Base Bid								\$	5,601.00
Altamata	#1	Cond 9 Definish Ma	land Flans			ADD.		•	
Alternate:	#1	Sand & Refinish W	000 F100r			ADD:	TOTAL	<b>3</b>	7,504.00
Voluntary Alt:							TOTAL		\$13,105.00
Voluntary Alt: Alternate No.									
Alternate No.							<del></del>		
Exclusions:									
Qualifications:	Alternat	be preformed during note #1: Included is sandir	ng and applying due to the dens	a clear wate sity of the wo	r or oil based fir od and inability	to evenly ac			floors
	Includ	led in ALT #1: 216 sf of	Red Oak Floorin	ng for Patchi	ng Existing Woo	d Flooring.			
Thank you for th	e opportu	nity to bid with you on this	s project. We loo	ok forward to	vorking with you.				
		Sincerely							
		0	_						
		Yan	mes s	Sper	rcer				

James Spencer, Project Manager

Notes:



### HISTORIC HARTMAN HOUSE AT HOGTOWN CREEK HEADWATERS

A. BID PACKAGE SAVINGS & BUYOUT TO DATE 23A MECHANICAL/HVAC

23A	MECHANICAL / HVAC					
	Renovations per plans or as outlined on cover page.	LS	1	\$13,885.00	\$13,885.00	

ORIGINAL ESTIMATE: \$13,885.00

LESS CONTRACT: \$13,582.00

BID PACKAGE SAVINGS: \$ 303.00



#### CMC1250445

PO Box 1329 Belleview FL 34421 3524212913 Info@hvacfla.com

# ESTIMATE# 1181 DATE 01/30/2020 PO#

**Estimate** 

### **CUSTOMER**

J.E. Decker Construction Karlin Warkentin (352) 318-9149

### **SERVICE LOCATION**

J.E. Decker Construction Karlin Warkentin Hartman House

(352) 318-9149

_		
Base	hı	∩ .
Dasc	U	u-

\*Includes load calcs, Permit with City of Gainesville, and drawings.

### DX split system:

- \*Trane 5Ton 14 SEER, Heat pump, Air Handling unit
- \*Pre fab concrete pad
- \*Stand-alone controls
- \*Soft copper refrigerant lines with ¾" insulation (to be concealed in wall)
- \*Drain pan, aux. float switch
- \*PVC drain line with 1/2" insulation

### Duct system:

- \*1.5" duct board for SA and RA trunks;
- \*Lateral flexible lines to grilles;
- \*Insulated boots for grilles;

### **DESCRIPTION**

- \*Grille (white);
- \*8" Outside Air run with 10"x10" filter back grill;

### Exhaust system:

- \*(1) Broan 4000 Series 30" under cabinet range hood (stainless steel);
- \*Side vent exhaust with birds screen for range hood and associated duct;
- \*(2) NuTone 80CFM ceiling exhaust fan in each bathroom;
- \*(2) 4" Side vent exhaust cap with back draft damper for EF's;

Bade Bid: \$13,582.00

Deduct: \$843 for Run Tru by Trane equipment.

Alt 1 - Certified Test and Balance: \$950.00

Alt 2 - combine both bath fans to (1) 8" side vent in lieu of (2) 4" side vents. : \$450.00

Description Qty Rate Total

CUSTOMER MESSAGE Estimate Total: \$0.00



# CHANGE ORDER #4 HISTORIC HARTMAN HOUSE AT HOGTOWN CREEK HEADWATERS

B.PROVIDE AND INSTALL NEW SIDING DUE TO CONDITIONS OF EXISTING SIDING AFTER DEMOLITION STARTED. EXISTING SIDING WAS ORIGINALLY PLANNED TO REMAIN WITH MINOR CARPENTRY WORK TO RESTORE BUT PROJECT TEAM CONCLUDED THAT LEAVING THE EXISTING SIDING WAS NOT FEASIBLE DUE TO CONDITION. ALSO THE DISCOVERY OF THE T&G INTERIOR WOOD WALL PANELING NECESSITATED REMOVING THE FAILING SIDING TO BE ABLE TO ROUGH-IN ELECTRICAL AND INSULATE THE WALLS (WHICH THE LATER IS REQUIRED PER CODE). PLEASE REFER TO ARCHITECT'S SCOPE USED FOR PRICING THE GMP ON THE FOLLOWING PAGES STATING THAT "THE EXTERIOR SIDING IS OVER ALL GOOD, IN NEED OF PAINT AND CAULK". WE UNDERSTAND THIS TO BE **ABOVE AND BEYOND ROUGH&FINISH CARPENTRY THAT WAS INCLUDED IN THE GMP**.

MATERIAL ALLOWANCE FOR FASTNERS & TRIM NECESSARY TO COMPLETE SIDING INSTALL: \$1,500.00 PLUS MATERIALS ALREADY PURCHASED:\$4,085.00

TOTAL MATERIALS ALLOWANCE: \$5,585.00

**B. SIDING ABOVE** AND BEYOND **ROUGH&FINISH** CARPENTRY THA **WAS** INCLUDED IN T GMP.

# **Quote/Invoice**

### Howell Logging, Inc. **DBA**

### **CRACKER STYLE LOG HOMES**

20253 NE 20th St Williston FL 32696 Ph: (352)529-2070 Fax: (352)528-3777



Name: J E Decker Construction 2/14/2020 Address: City/State: Phone 352 318 9149 Fax: GLC

		LoriB@Jedeckerconstruction.com				
Qty	Units	Description	Designation	Unit Price		Total
5730		2500 sq ft =5730 LF No waste  1x6 Special Novelty Blue streak Pine  All material sold as randon length Random length can be (4'-16') material  Deposit required  \$2,042.43 ck#5580		\$	\$\$\$ \$\$\$\$\$\$\$\$\$\$\$\$\$\$\$\$\$\$\$	- - - - - 3,724.50 - - - - - - - - - - -
		All meterials must be picked up within	20 days	\$ -	\$	2 724 50
		All materials must be picked up within		Material Total	l .	3,724.50
		after placing order, if not material will	_	P&H	1 '	93.11
		in inventory and your deposit will be lo	ost.	Sub-Total	1	3,817.61
		All sales are final, no refunds.		FL. Tax		267.23
				Delivery		
				Total	\$	4,084.85

\*Important: All Checks payable to Howell Logging, Inc.

50% down to start order and balance before pickup or delivery

Must have machine or manpower to unloa if we deliver.

\$4,085.00 **ROUNDED TO** NEAREST WHOLE **DOLLAR** 



# Quote/Invoice

**B. SIDING ABOVE** AND BEYOND ROUGH&FINISH **CARPENTRY TH** WAS INCLUDED IN TH GMP.

### Howell Logging, Inc. DBA

### **CRACKER STYLE LOG HOMES**

20253 NE 20th St Williston FL 32696 Ph: (352)529-2070 Fax: (352)528-3777



Name: J E Decker Construction	2/14/2020
Address:	2/14/2020
City/State:	
Phone 352 318 9149	
Fax:	GLC

	Email	LoriB@Jedeckerconstruction.com			1202	
Qty	Units	Description	Designation		T	otal
				\$ - \$ -	\$ \$	-
		2500 sq ft =5730 LF No waste		\$ - \$ - \$ -	\$ \$ \$	-
5730	LF	1x6 Special Novelty Blue streak Pine		\$ 0.65 \$ - \$ -	\$ \$ \$ \$ 6	3,724.50 - -
		All material sold as randon length Random length can be (4'-16') material		\$ - \$ - \$ -	\$ \$ \$	-
		Deposit required		\$ - \$ - \$	\$ \$ \$	-
				\$ - \$ - \$ - \$ -	\$ \$ \$ \$	-
	-	All materials must be picked up within	30 days	Material Total	\$	2 704 50
		after placing order, if not material will	go back	P&H	7	3,724.50 93.11
		in inventory and your deposit will be lo	st.	Sub-Total	\$	3,817.61
		All sales are final, no refunds.		FL. Tax Delivery	\$ FOB Mill	267.23
	4 411	Checks payable to Howell Larging In-		Total	THE RESERVE TO SHARE THE PARTY OF THE PARTY	4,084.85

\*Important: All Checks payable to Howell Logging, Inc.

50% down to start order and balance before pickup or delivery

Must have machine or manpower to unload if we deliver.

HISTORIC HARTMAN HOUSE AT HOGTOWN CREEK HEADWATERS

B<sup>'</sup>,PROVIDE AND INSTALL NEW SIDING DUE TO CONDITIONS OF EXISTING SIDING AFTER DEMOLITION

STARTED. EXISTING SIDING WAS ORIGINALLY PLANNED TO REMAIN WITH MINOR CARPENTRY WORK TO RESTORE BUT PROJECT TRAM CONCLUDED THAT LEAVING THE EXISTING SIDING WAS NOT FEASIBLE DUE TO CONDITION. ALSO THE DISCOVERY OF THE T&G NECESSITATED REMOVING THE FAILING SIDING TO BE ABLE TO ROUGH -IN ELECTRICAL AND INSULATE THE WALLS WHICH IS REQUIRED PER CODE. PLEASE REFER TO ARCHITECT'S SCOPE USED FOR PRICING THE EMP ON THE NEXT PAGE STATING THAT "THE EXTERIOR SIDING IS OVER ALL GOOD, IN NEED OF PAINT AND CAULK". WE UNDERSTAND THIS TO BE ABOVE AND BEYOND ROUGH&FINISH CARPENTRY THAT WAS INCLUDED IN THE GMP.

### JAY REEVES & ASSOCIATES, INC.



ARCHITECTS AND DESIGNERS
725 NORTHEAST 1<sup>ST</sup> STREET
GAINESVILLE, FLORIDA 32601

WWW.JAYREEVES.COM

FAX 352.505.5689

# RENOVATION EVALUTION REPORT HARTMAN HOUSE

### DEPARTMENT OF RECREATION & PARKS CITY OF GAINESVILLE NATURE OPERATION DIVISION AUGUST 20, 2010

The Hartman house is an early 20<sup>th</sup> century wood frame vernacular farmhouse that is central to a tract of land located in North West Gainesville.

The structure C.A, 1910 is a simple vernacular residential structure that has been expanded at least once. The original shape appears to be "T" shaped with service rooms to the rear. The rear wing with flanking porches appears to have been extended and the side porches added at different times. The original house likely consisted of 3 main rooms, a full width front porch, and rear wing side chimney that originally supplied heat, along with an oil burning heater at the dining room. There currently is no airconditioning.

The house sits approximately 30" above grade with wood floors, oak over pine in the main rooms; windows are traditional wood double hung 2 over 2 sashes. Siding is wood novelty type roofing is asphalt shingle, original cypress shake.

The house is single story comprised of 7 primary rooms and 3 minor rooms and 2 large screened porches and 1 small-screened porch.

The building square footage is 1780 sq. ft. interior space and 600 sq.ft. open porches.

### **EXISTING CONDITIONS:**

The building is vacant with no active utilities. The overall structural condition is fair, in need of paint, and urgent need of a new roof, and some associated deck and fascia repair.

The building is secure with several broken windows including glass in 2 doors, several damaged interior doors as a result of recent vandals.

The most significant roof damage is at the lower roof over the North porch, there is evidence of damaged roof deck, and damaged porch flooring. The current roof is multiple

# B. SIDING ABOVE AND BEYOND ROUGH&FINISH CARPENTRY THAT WAS INCLUDED IN THE GMP.

layers, explaining the lack of leaks over the main portion of the house. The North porch was recently covered with roll roofing to stop active leaks and damage. Most exterior window are not boarded. The surrounding vegitation is in need of trimming to keep moisture down. The foundation is open and will need to be closed in with wood grills to keep animals out and meet building codes. The steps at all entrances do not have proper landings and do not meet code for rise and run, or handrails.

Structurally the building is in good condition for its age. Where additions or alterations were made in the past, the structure should be examined as this is often inferior work to the original structue. Any structural damage should be limited to the porch areas where damage is evident. Bathroom floors, especially beneath the tub are often damaged and should be inspected.

### **EXTERIOR CONDITIONS:**

The exterior siding is over all good, in need of paint and caulk Exterior windows need paint, window sashes need putty and to be re-glazed. Window screens need to be replaced and some reattached. The windows at the South porch were poorly adapted recycled window that do not fit or completely seal. These windows should be replaced entirely.

All exterior porches need new screen and flooring repair/replacement.

The exterior chimneys brickwork is in good condition, but should be capped to keep animals and rain out.

Currently there is cast iron and steel plumbing and metal electrical conduit on the exterior surfaces that should be relocated inside the walls.

The wood floor structural system is supported on brick piers located typically on 8 foot or less centers.

Some exterior brick piers at the outside perimeter show mortar deteriorate with some leaning noticeably, these deteriorated piers should be reconstructed with concrete pad footings added where they are failing.

Interior public rooms may require addition support due to ''DESIGN'' for residential loading.this can be achieved by adding 1 or 2 new mid-joist supporting beams, on concrete block piers, on concrete pads beneath the rooms in question.

This floor load remediation applies to porches as well since they are gathering points for the public, and typically under structured.

### **INTERIOR CONDITIONS:**

The interior finishes are in fair condition; walls and ceiling could be salvaged.



# B. SIDING ABOVE AND BEYOND ROUGH&FINISH CARPENTRY THAT WAS INCLUDED IN THE GMP.

**CHANGE ORDER #4** 

HISTORIC HARTMAN HOUSE AT HOGTOWN CREEK HEADWATERS B.

PROVIDE & INSTALL NEW SIDING - ABOVE AND BEYOND ORIGINAL SCOPE

07 SIDING LABOR ALLOWANCE

CARPENTER FOREMAN \$1,600.00 FOR 1.5 WEEKS = \$2,400.00

CARPENTER \$1,520.00 FOR 1.5 WEEKS = \$2,280.00

CARPENTER'S HELPER \$ 770.00 FOR 1.5 WEEKS = \$1,155.00

TOTAL SIDING LABOR ALLOWANCE: \$5,835.00



# CHANGE ORDER #4 HISTORIC HARTMAN HOUSE AT HOGTOWN CREEK HEADWATERS C. PROVIDE & INSTALL ADDITIONAL WINDOW TRIM AND INTERIOR TRIM WORK


### 06 MATERIAL AND LABOR ALLOWANCE - ABOVE AND BEYOND ORIGINAL SCOPE.

CARPENTER FOREMAN X 2 @\$40.00/EACH FOR 10 HOURS FOR 2 DAYS = \$1,600.00

CARPENTER'S HELPER FOR 2.5 WEEKS \$768.00/WEEK = \$1,920.00

MATERIALS ALLOWANCE = \$3,500.00

TOTAL MATERIAL AND LABOR ALLOWANCE: \$7,020.00

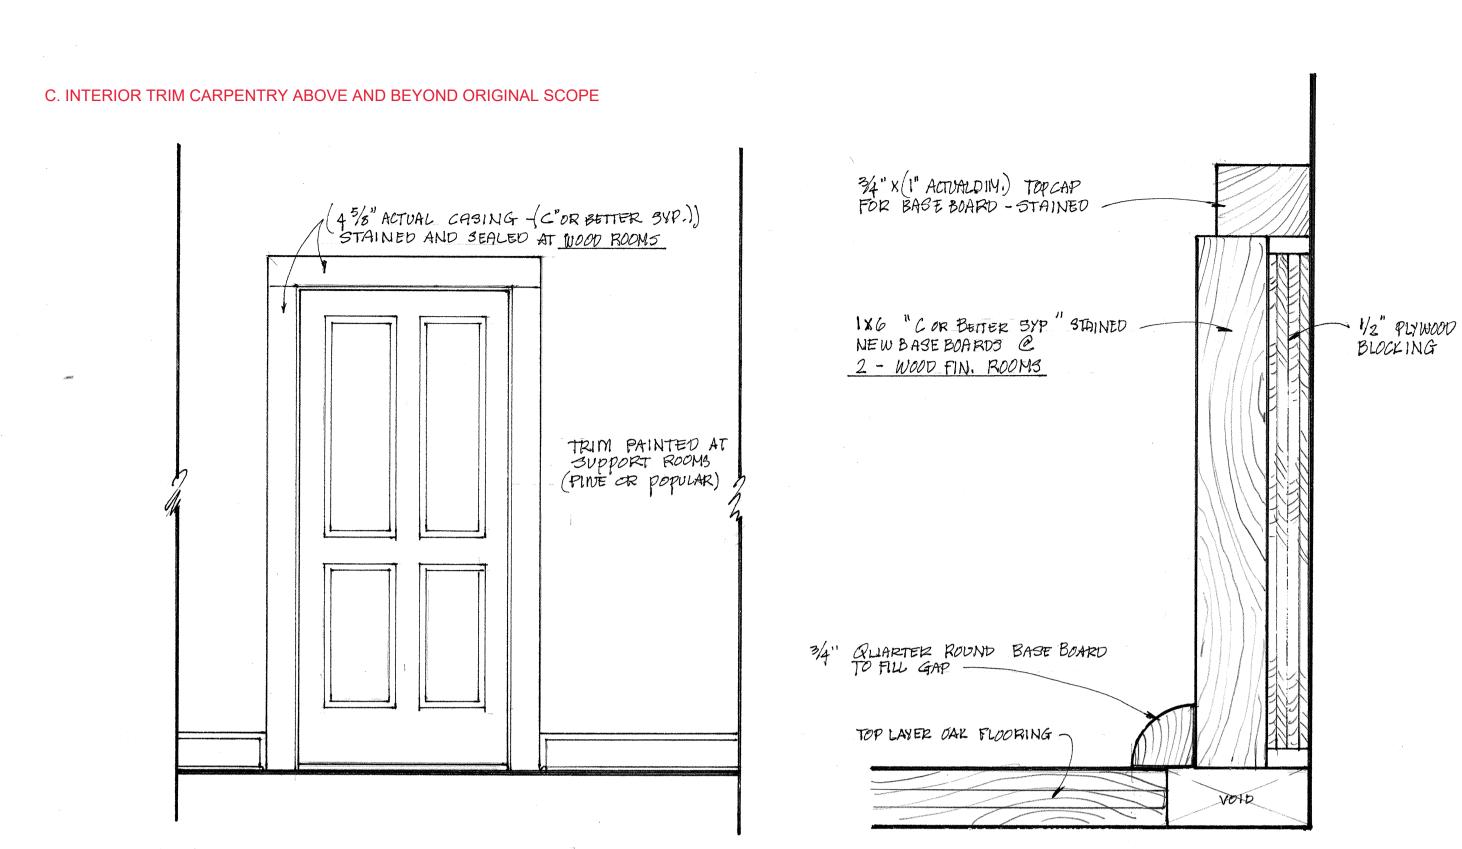

1x45/8" Cor Better 5YP - STAINED

CONBETTER SYP.

- ORIGINAL SABHES -

DOOR CASING. TOP & END CAP. GIXE "C OR BETTER SYP" STAINED W/ 2 COATS SATIN 34" QUARTER ROUND BASE BOARD TO FILL GAP.

# BASE BOARD ELEVATION @ DOOR CASING SCALE: FULL SIZE

# INTERIOR DOOR CASINGS

SCALE: 3/4" =1'-0"

1×4 % PINE OR
POPULAR@ PAINTED
TRIM SUPPORT ROOMS

POPULAR OR
PINE WINDOW SILL
PAINTED

1 x 45/8 PINE - PAINTED -

@ PAINTED TRIM

SUPPORT ROOMS,

# BASE BOARD SECTION @ TWO WOOD ROOMS SCALE: FULL SIZE

-GALY. MIL FLASHING EXTERIOR 2X 456" PINE OIL PRIMED AND 2 FINISH COATS & SEALED @ WOOD ROOMS -STOPS CUT TOORIGINAL PAINTED - INC. INSIDE AND OUTSIDE FRAME WINDOW SILL CUT TO MATCH ORIGINAL PITCHED 2X PT WINDOW JILL OIL PRIMED AND 2 FINISH COATS -1x4% C or BETTER SYP STAINED & SEALED

NO PRIOR INTERIOR TRIM OR DIRECTION FOR THIS IN ORIGINAL GMP

CASINGS & BASEBOARD TRIM 3-12-20


# WINDOW INTERIOR TRIM

SCALE: 3/4" =1'-0"

# WINDOW EXTERIOR TRIM

SCALE: 3/4" =1'-0"

# JAY REEVES ARCHITECT LLC.



### C. INTERIOR TRIM CARPENTRY ABOVE AND BEYOND ORIGINAL SCOPE

layers, explaining the lack of leaks over the main portion of the house. The North porch was recently covered with roll roofing to stop active leaks and damage. Most exterior window are not boarded. The surrounding vegitation is in need of trimming to keep moisture down. The foundation is open and will need to be closed in with wood grills to keep animals out and meet building codes. The steps at all entrances do not have proper landings and do not meet code for rise and run, or handrails.

Structurally the building is in good condition for its age. Where additions or alterations were made in the past, the structure should be examined as this is often inferior work to the original structue. Any structural damage should be limited to the porch areas where damage is evident. Bathroom floors, especially beneath the tub are often damaged and should be inspected.

### **EXTERIOR CONDITIONS:**

The exterior siding is over all good, in need of paint and caulk. Exterior windows need paint, window sashes need putty and to be re-glazed. Window screens need to be replaced and some reattached. The windows at the South porch were poorly adapted recycled window that do not fit or completely seal. These windows should be replaced entirely.

All exterior porches need new screen and flooring repair/replacement.

The exterior chimneys brickwork is in good condition, but should be capped to keep animals and rain out.

Currently there is cast iron and steel plumbing and metal electrical conduit on the exterior surfaces that should be relocated inside the walls.

The wood floor structural system is supported on brick piers located typically on 8 foot or less centers.


Some exterior brick piers at the outside perimeter show mortar deteriorate with some leaning noticeably, these deteriorated piers should be reconstructed with concrete pad footings added where they are failing.

Interior public rooms may require addition support due to ''DESIGN'' for residential loading.this can be achieved by adding 1 or 2 new mid-joist supporting beams, on concrete block piers, on concrete pads beneath the rooms in question.

This floor load remediation applies to porches as well since they are gathering points for the public, and typically under structured.

### **INTERIOR CONDITIONS:**

The interior finishes are in fair condition; walls and ceiling could be salvaged.

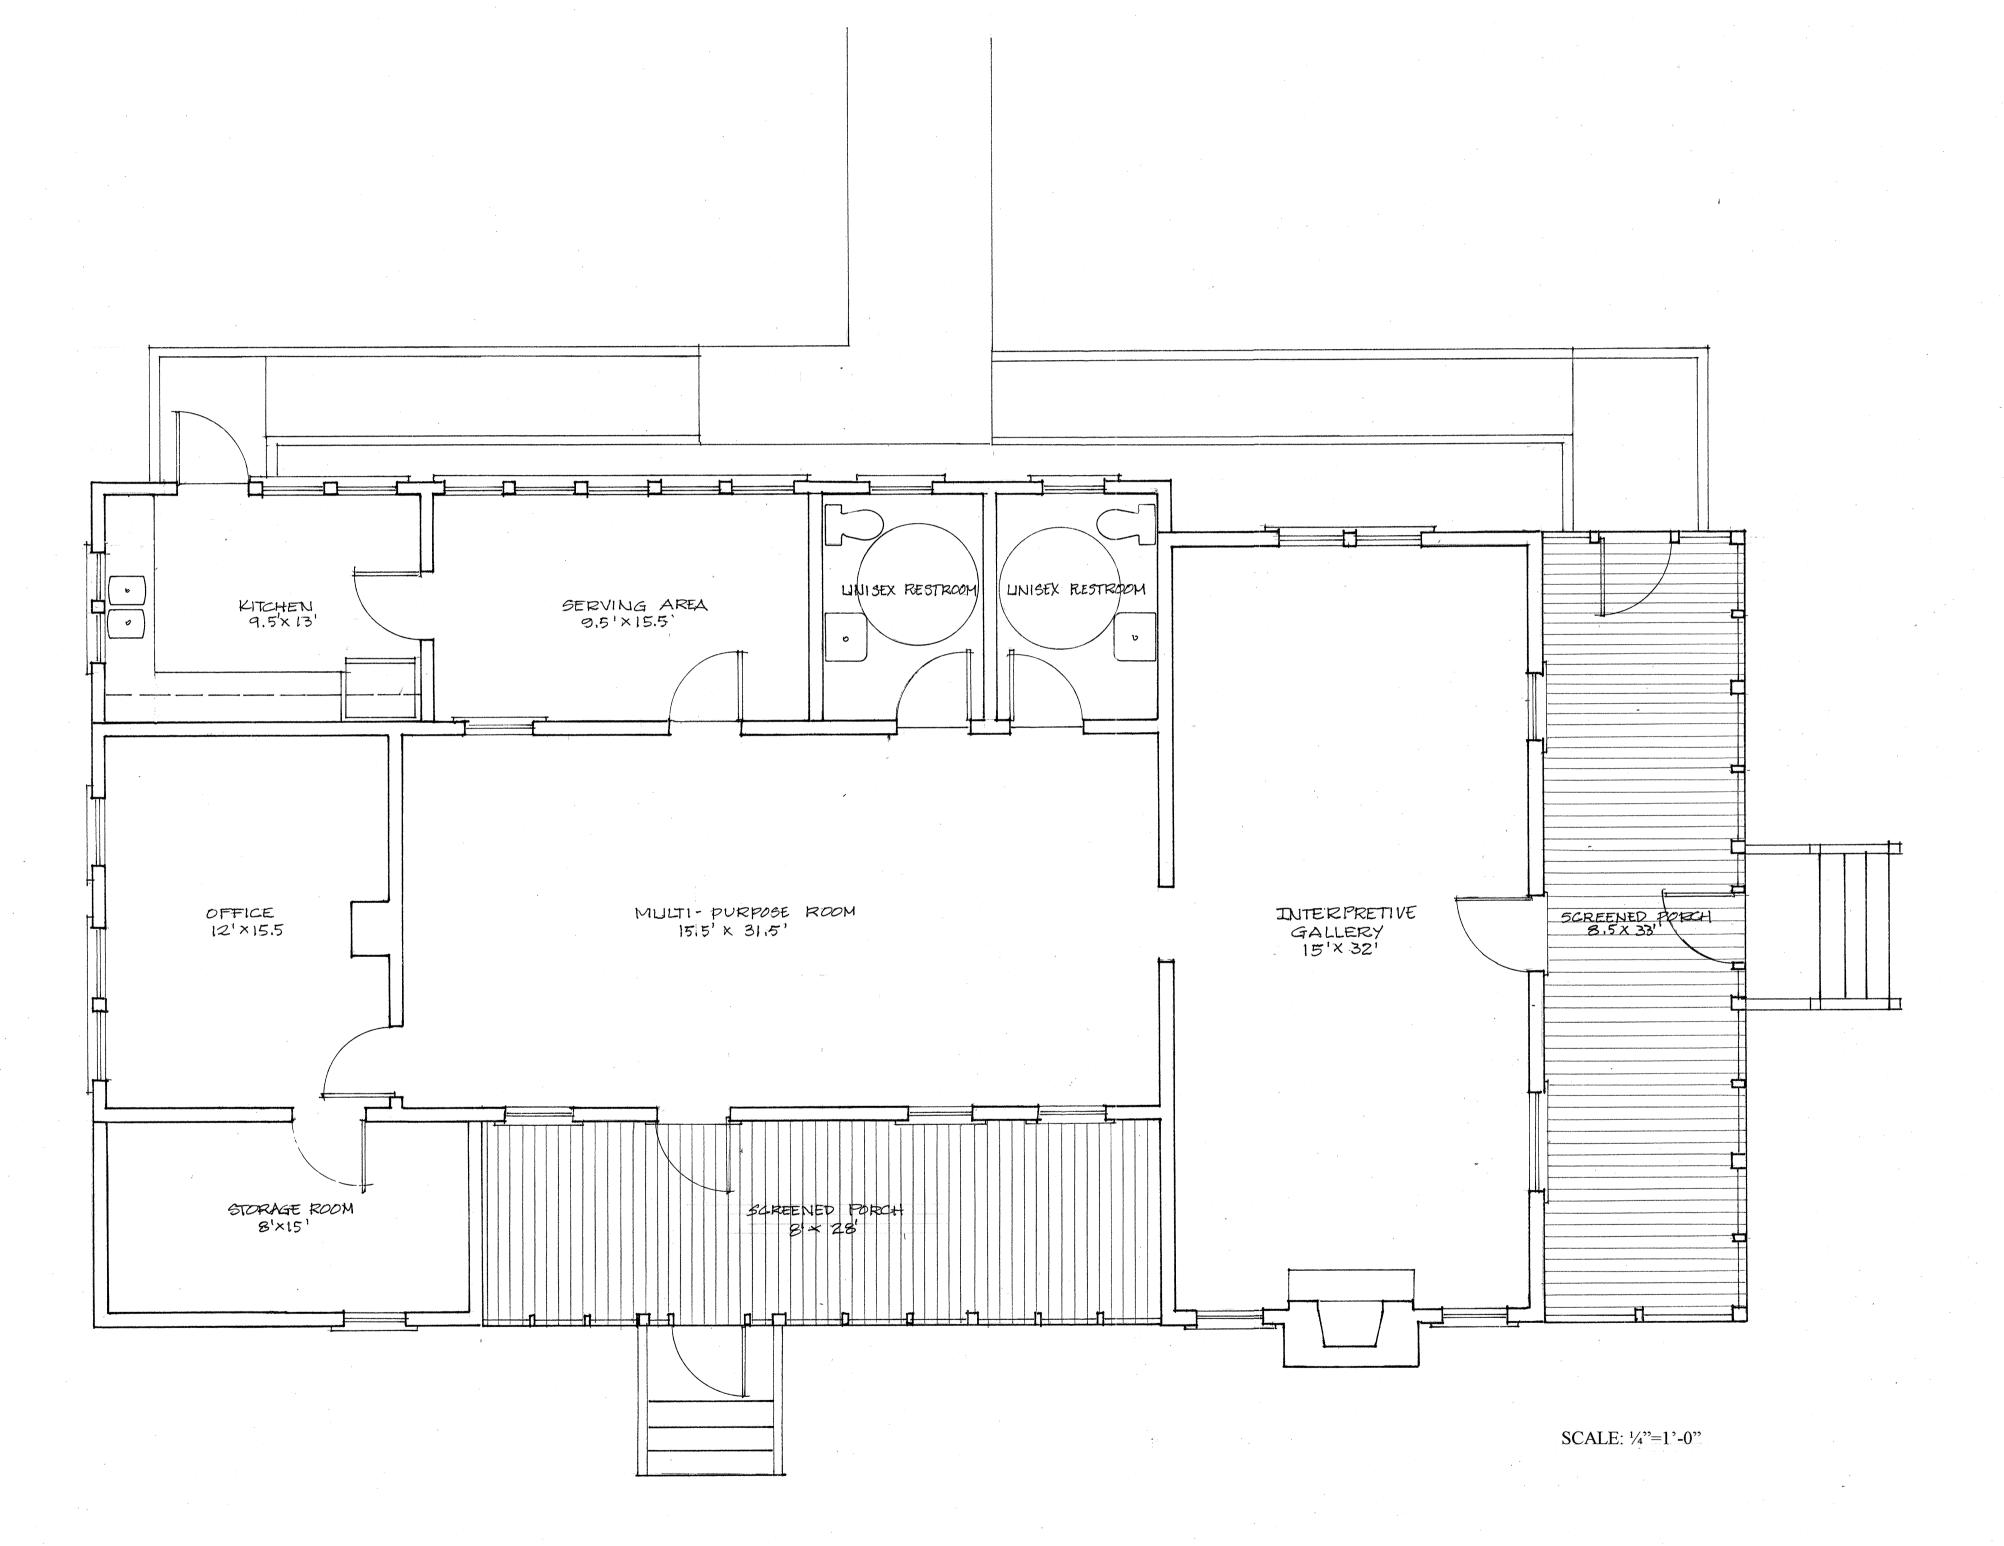

### E. User Group driven changes

### HARTMAN HOUSE APPLIANCES FINAL SELECTIONS

HOME DEPOT	BUDGET	
REFRIDGERATOR		
GE 24.7 CU.FT. FRENCH DOOR MODEL#GNE25JGKWW	\$ 1,619.10	
Parts & Service 12' Upgraded Braided Water Line	\$ 17.28	
RANGE		
GE 5.3 CU.FT. ELECTRIC RANGE MODEL#JB750DJWW	\$ 908.10	
Power Cord	\$ 25.98	
DISHWASHER		
BOSCH 100 SERIES MODEL#SHEM3AY52N	\$ 449.10	
BOSCH DISH JUNCTION BOX	\$ 29.98	
DISWASHER PARTS KIT & ADAPTER	\$ 21.98	
DISHWASHER INSTALL	\$ 150.00	
SUBTOTAL	\$ 3,221.52	
7% SALES TAX	\$ 225.51	
TOTAL	\$ 3,447.03 \$ 2,500.0	00
PRICE INCLUDES DELIVERY & INSTALLATION	ROUNDED UP \$948.00 OVER BUDGET	7

RECEIPTS AND/OR INVOICES WILL BE PROVIDED FOR ALL ITEMS AT TIME OF INVOICING

# Del Sol Electric, LLC

EC13004859

3515 NW 12th Ave Gainesville, FL 32605 US (352)514-2177 delsolelectric13@gmail.com

# Del Sol Electric...

**Estimate** 

### **ADDRESS**

Karlin Warkentin J. E. Decker Construction Group, LLC 1503 NW 16th Ave Gainesville, FL 32605

**ESTIMATE #** 1165 **DATE** 03/09/2020

### **JOB NAME**

Hartman House

ACTIVITY	QTY	RATE	AMOUNT
Change Order We will provide labor and material to install the following; • install underground 2" pvc conduit for commutation main line from UGB to room 108 N wall. • for network cabling purposes, install three 4sq boxes single gang rings and 1" conduits to accesible ceiling area in room 103. •install a 120 volts 20 amps circuit/ quad receptacles outlets in north wall of NE storage building. • install a 4sq box with a single gang ring and 1" conduit for commutation cable in classroom 101 N wall next to existing receptacle outlet. • add two floor boxes, 101 classroom and 105 staff lunch room.	1	1,850.00	1,850.00
	TOTAL		\$1,850,00

Accepted By

**Accepted Date** 

HISTORIC HARTMAN HOUSE AT HOGTOWN CREEK HEADWATERS

F. STAFFING/GENERAL CONDITIONS FOR CHANGES TO DATE

JEDCG SUPERINTENDENT VEHICLE/EQUIPMENT

ASSI. Superintendent - 1/4 i ime for o ivionins	нк	220	\$32.50	\$7,15U.UU
Superintendent Equipment (Cell, Tablet/Laptop, Vehicle, ETC.)	MO	3	\$850.00	\$2,550.00
1			4.4.4	

\$8,120.13 supervision allowances based on previous billings projected out for 4 weeks. If allowance happens to be unused it can be returned to project.

HISTORICAL HARTMAN HOUSE AT HOGTOWN CREEK HEADWATERS

G. DOOR SCOPE CHANGE DUE TO CONDITIONS OF EXISTING DOORS

ORIGINAL SCOPE WAS FOR 6 NEW INTERIOR DOORS AND REPAIR OF 3 EXISTING EXTERIOR DOORS. FINAL SCOPE INCLUDED 12 NEW DOORS.

INCLUDES VALUE-ENGINEERED (VE) DOORS PACKAGE.

### **THIS IS ABOVE AND BEYOND ORIGINAL SCOPE**

WARE				
or as outlined on cover page.	OPENING	6	\$250.00	\$1,500.00
OF NEW DOORS / HARDWARE				
or as outlined on cover page.	OPENING	6	\$150.00	\$900.00
S TO REPAIR EXISTING DOORS TO REMAIN				
or as outlined on cover page.	OPENING	3	\$250.00	\$750.00
L	or as outlined on cover page. LOF NEW DOORS / HARDWARE or as outlined on cover page. S TO REPAIR EXISTING DOORS TO REMAIN or as outlined on cover page.	or as outlined on cover page.  L OF NEW DOORS / HARDWARE or as outlined on cover page.  S TO REPAIR EXISTING DOORS TO REMAIN	or as outlined on cover page. OPENING 6  L OF NEW DOORS / HARDWARE or as outlined on cover page. OPENING 6  S TO REPAIR EXISTING DOORS TO REMAIN	or as outlined on cover page.  Description of the page

TOTAL: \$ 3,150.00

LESS QUOTE \$14,426.16

(\$11,276.16) MATERIALS OVERAGE

### TAYLOR, COTTON, & RIDLEY, Inc.

### DOORS, HARDWARE, & BUILDING SPECIALTIES

G. DOOR SCOPE CHANGE DUE TO CONDITION OF EXISTING DOORS. ORIGINAL SCOPE WAS FOR 6 NEW INTERIOR DOORS AND REPAIR OF 3 EXISTING EXTERIOR DOORS. FINAL SCOPE INCLUDED 12 NEW DOORS - INCL. VALUE ENGINEERED DOORS PACKAGE - ABOVE AND BEYOND ORIGINAL SCOPE

4410 S.W. 35<sup>th</sup> Terrace Gainesville, FL 32608 P.O. Box 141090 32614-1090 Phone (352) 376-3600 FAX (352) 376-0901 dcole@taylorcottonridley.com

Date: March 30, 2020 TO: JE Decker Attn: Karlin Warkentin

RE: Historic Hartman House

Taylor, Cotton & Ridley, Inc. is pleased to provide a quotation for the above referenced project as follows:

### SECTION 08110 – STANDARD STEEL DOORS AND FRAMES:

0 each Hollow metal frames — none specified 0 each Hollow metal doors — none specified

### **SECTION 08211 – FLUSH WOOD DOORS**

**8 each Wood door leaves** – to be Simpson manufacturer. Interior doors to be 4 panel design. All prepped to received hinges and cylindrical lockset. Door manufacturer will supply the glass. Frames and doors quoted as primed – field finish to be by others.

\*Excluding any/all installation

### FIBERGLASS DOORS

**4 each Fiberglass** - Exterior door to be 2 panel with half glass design. Fiberglass frames and doors with equivalent design as Simpson. Unfinished material – field finish to be by others. Prepped for applicable hardware.

\*Excluding any/all installation

### **SECTION 08700 - FINISH HARDWARE:**

**12 hardware sets as specified** – hinges to be supplied by pre-hung manufacturer. Cylindrical locksets to be Sargent. Closers to be LCN. Rim exit device to be Sargent. Flush bolts and wall stop to be Rockwood. All finished to be brushed chrome/stainless steel/aluminum as applicable.

\*Excluding any/all installation

### TAYLOR, COTTON, & RIDLEY, Inc.

### DOORS, HARDWARE, & BUILDING SPECIALTIES

4410 S.W. 35<sup>th</sup> Terrace Gainesville, FL 32608 P.O. Box 141090 32614-1090 Phone (352) 376-3600 FAX (352) 376-0901 dcole@taylorcottonridley.com

### NOTE:

We are bondable; however, a bond has not been included.

We acknowledge addendum #......

We exclude all overhead-roll up doors

We exclude all installation.

We exclude all glass and glazing unless noted above.

We exclude all aluminum doors and hardware unless noted above.


We exclude finish paint unless otherwise noted above.

We exclude the drilling and tapping for surface applied hardware.

We exclude the receiving, unloading, of materials unless we are performing installation; then we receive and store anything we are installing.

TOTAL COMBINE QUOTATION IN THE AMOUNT OF \$14,426.16 \*Tax included

minus \$3,150 total original doors allowance =\$11,276.16 change order request.

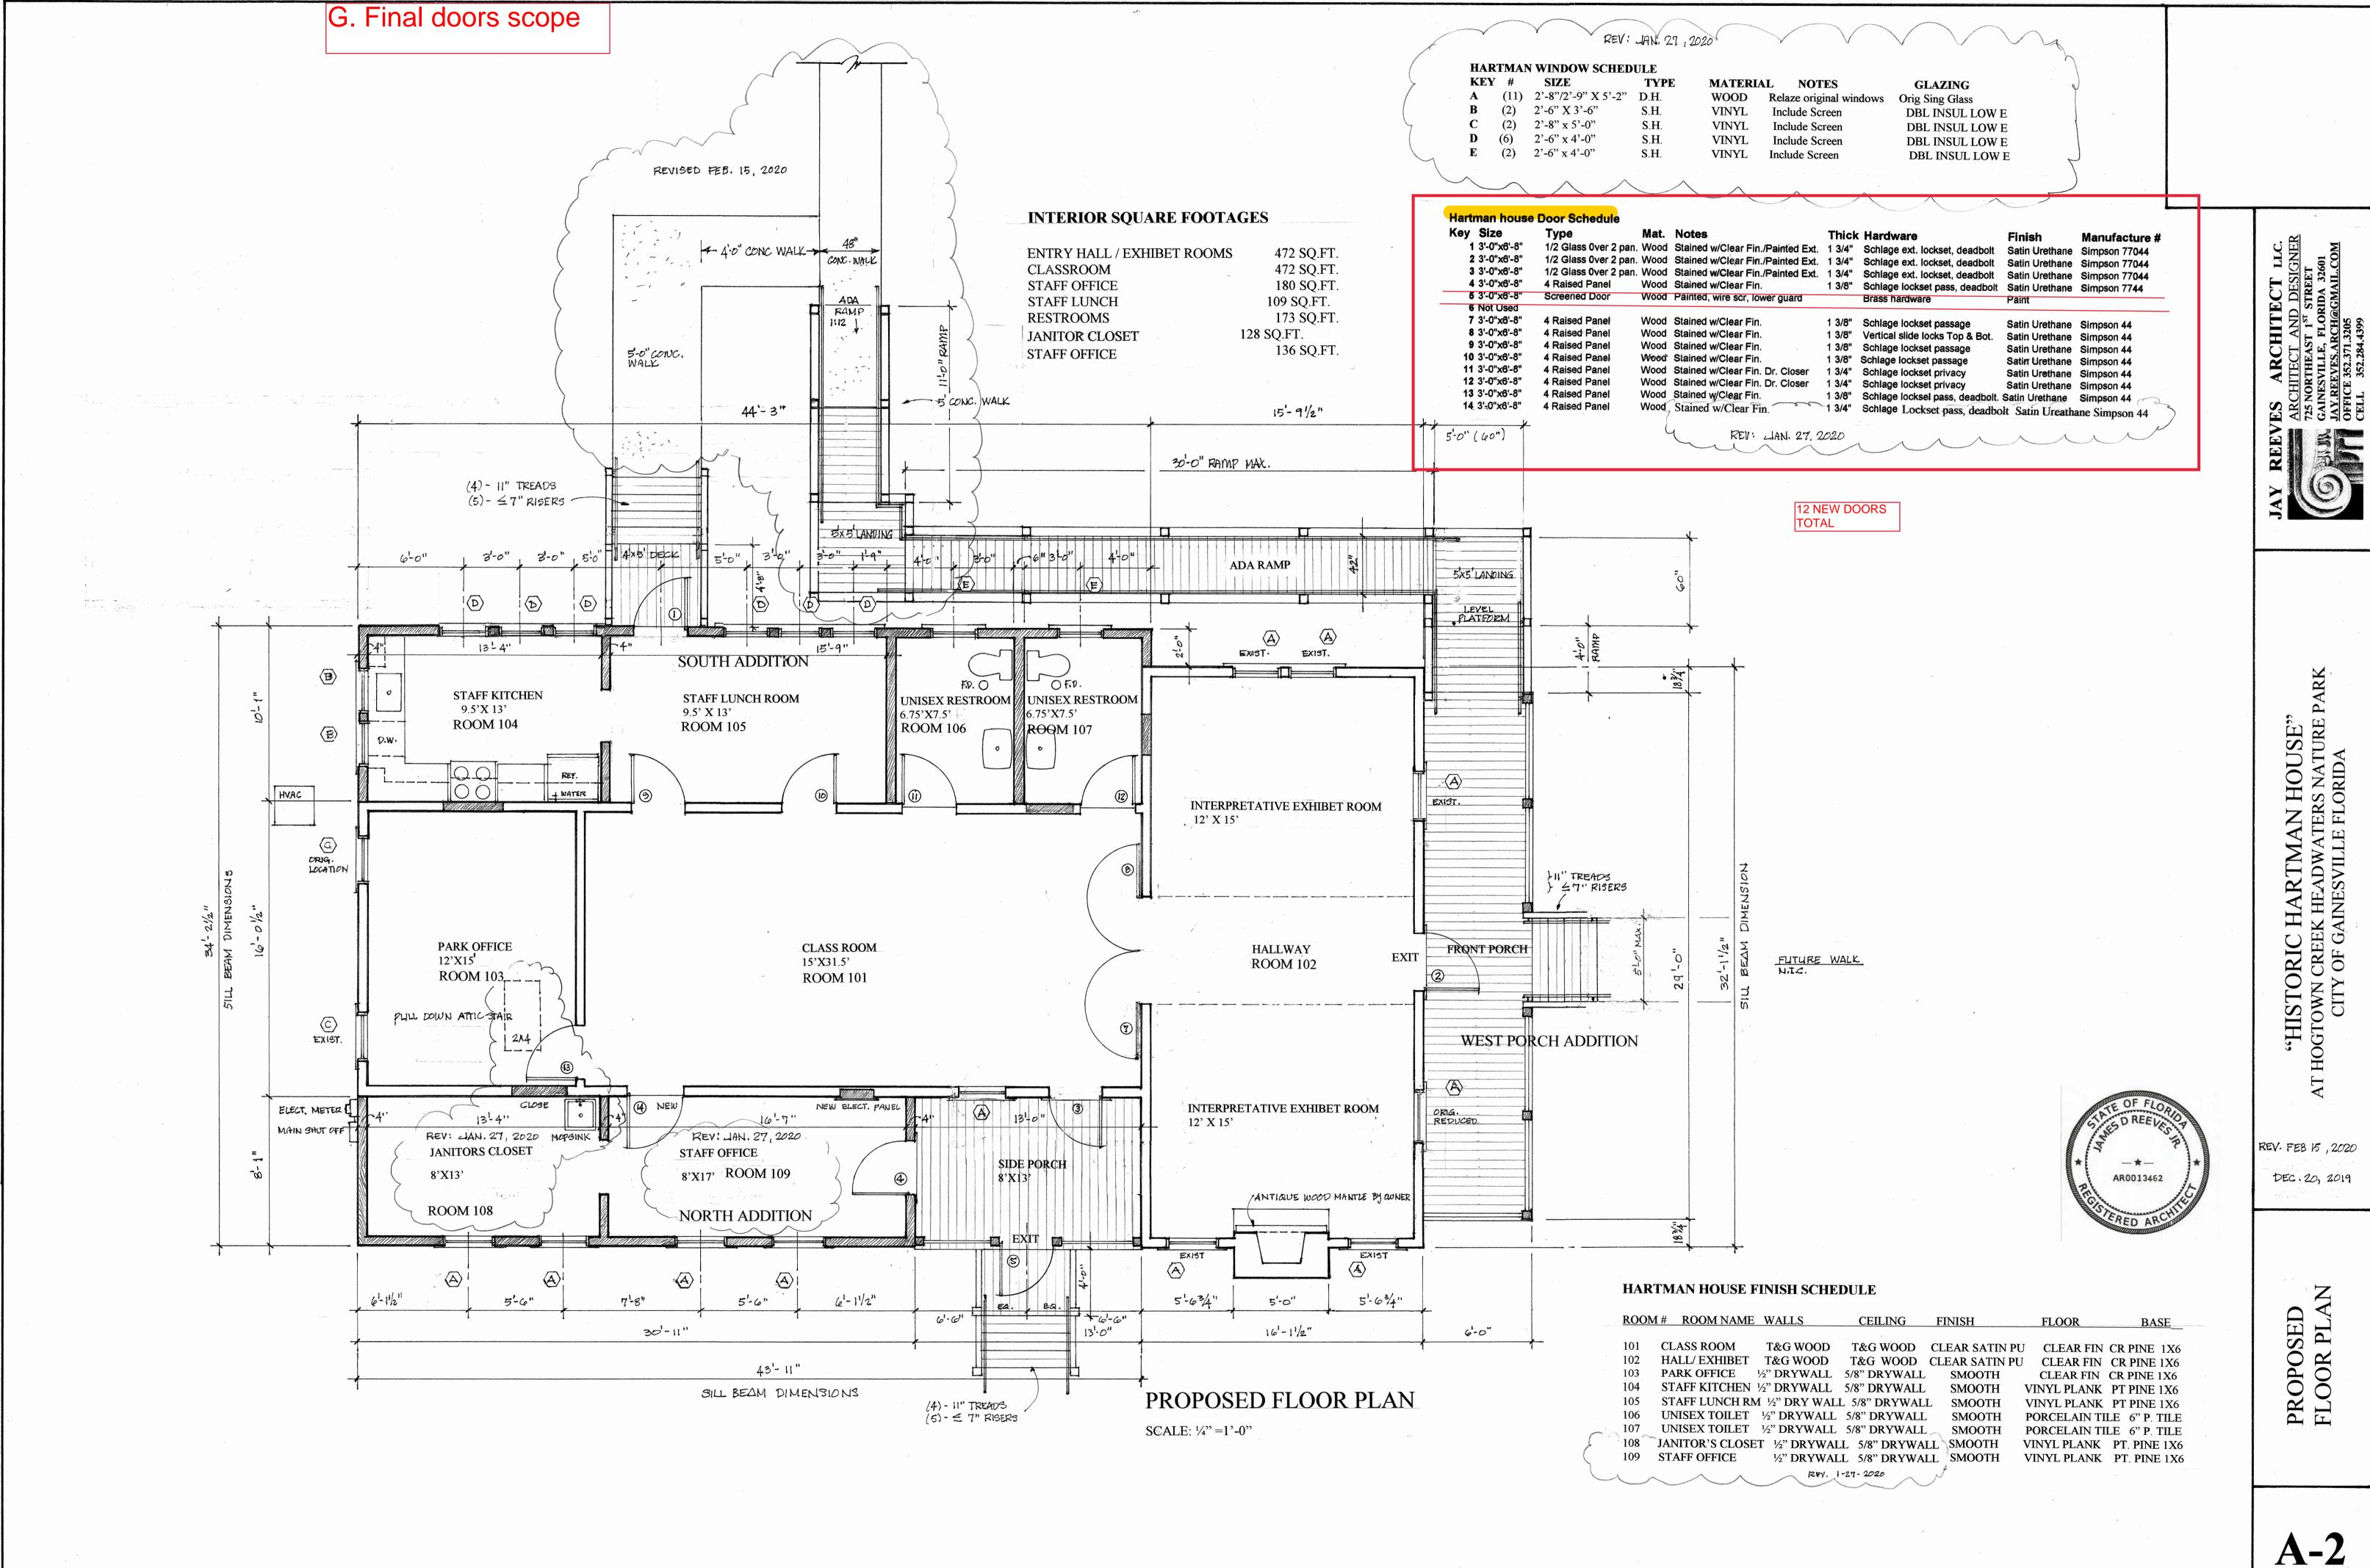

### G. Original doors scope

The wall finishes are drywall over the original plaster and lath or possibly bead board. There most likely is no insulation in the walls, rewiring may require opening all wall cavities. Attic insulation is minimal and needs replacement.

Interior wiring is a mixture of early wiring and later C.A 1970's, and the service will not support HVAC or meet code.

All interior wiring should be replaced and a minimum 200AMP service should be installed, to have handle HVAC equipment.

All interior plumbing is dated and should be replaced, the existing septic tank should be abandoned and a line run for city services.

All new central heat / air –split – heat pump system should be installed. The building needs all new insulation.

All existing windows need new locks, existing exterior door need new locks. The windows should be sealed except for a few desired to be operable.

Interior flooring should be refinished with the exception of the bath and kitchen which will likely need replacement.

Some interior doors can be reused except for rooms requiring ADA access where door width is a factor. There should be minimum 32 inches clear space at each door.

All existing lighting should be replaced with period style fixture in the public rooms and recessed fixtures elsewhere.

### **PROPOSED USE:**

The nature operation division has proposed the use of a public / office use that would act as the primary park building including restrooms for public use and or several display rooms for park / house interpretation.

Also with in the house will be located park office and lockable storage for equipment. These proposed uses are achievable with the renovation of this structure, and compatible with the historic nature of this building.

In addition to complete renovation, the building will need modification to provide for ADA accessibility. If rooms are used for display and expect more than 8 people per room, then floors should be reinforced for additional loading.

### **ADA COMPLIANCE:**

The structure is located 30" above grade and will require an exterior ramp, best located at the North porch entrance, which has good access to all interior areas. The two doors located off the North porch will need to be resized to 36 inches wide.

