The Brentwood Company, Inc.

Legislative *ID# 150640B*

ID	Task Name	Duration	Start	Finish
1	Begin Turbidity Monitoring Per SJRWMD ERP Conditions	2 days	Mon 1/18/16	Tue 1/19/16
2	Submit Sediment and Erosion Control Plan to Engineer	5 days	Mon 1/18/16	Fri 1/22/16
3	FDOT Construction Entrance Driveway Permit	5 days	Mon 1/18/16	Fri 1/22/16
4	Permitting	12 days	Mon 1/18/16	Tue 2/2/16
5	Construct Stabolized Construction Entrance	5 days	Mon 1/18/16	Fri 1/22/16
6	Install Construction Barrier, Silt Fence, Filter Barrier, Wattles, Etc...	5 days	Mon 1/18/16	Fri 1/22/16
7	Install Turbidity Control Measures in Tumblin CreeK	4 days	Wed 1/20/16	Mon 1/25/16
8	GRU Slipline	13 days	Tue 1/19/16	Thu 2/4/16
9	GRU Begin Pumping Around Line	1 day	Mon 1/18/16	Mon 1/18/16
10	Initial Grading for Equipment Access	3 days	Wed 2/3/16	Fri 2/5/16
11	Install N/S Sheet Piles	20 days	Mon 2/8/16	Fri 3/4/16
12	Grade Bypass Channel	4 days	Mon 3/7/16	Thu 3/10/16
13	Install Rip Rap at Bypass Channel	10 days	Fri 3/11/16	Thu 3/24/16
14	Install Temp Cofferdam to Divert Creek to Bypass Channel	2 days	Fri 3/25/16	Mon 3/28/16
15	Install EW Sheet Piling	5 days	Tue 3/29/16	Mon 4/4/16
16	Mass Excavation for Segmented Wall and Cast Wall	4 days	Tue 4/5/16	Fri 4/8/16
17	Construction of Cast Wall/Gate Foundation	6 days	Mon 4/11/16	Mon 4/18/16
18	Construct Cast in Place Wall	7 days	Tue 4/19/16	Wed 4/27/16
19	Construct Segmented Retaining Wall	14 days	Thu 4/28/16	Tue 5/17/16
20	Construct Gate Structure	8 days	Thu 4/28/16	Mon 5/9/16
21	Backfill at Segmented/Cast Wall	4 days	Wed 5/18/16	Mon 5/23/16
22	Rough Grade for Sediment Basin	4 days	Wed 5/18/16	Mon 5/23/16
23	Storm Structures and Piping	6 days	Tue 5/24/16	Tue 5/31/16
24	Final Grade/Compaction for Sediment Basin Slabs	4 days	Wed 6/1/16	Mon 6/6/16
25	Install Composit Piling for Trash Boom	2 days	Tue 6/7/16	Wed 6/8/16
26	Construct Concrete Slabs	15 days	Tue 6/7/16	Mon 6/27/16
27	Install Balance of Rip Rap	3 days	Tue 6/28/16	Thu 6/30/16
28	Install Trash Boom	5 days	Tue 6/28/16	Mon 7/4/16
29	Install Pneumatic Gate	5 days	Tue 6/28/16	Mon 7/4/16
30	Install Chain Link Fence	3 days	Tue 6/28/16	Thu 6/30/16
31	Construct Retention Ponds and Swales	6 days	Tue 6/7/16	Tue 6/14/16
32	Seed and Sod Disturbed Areas	3 days	Tue 7/5/16	Thu 7/7/16
33	Construct Paved Road	10 days	Wed 6/15/16	Tue 6/28/16
34	Final Grading of Site	4 days	Wed 6/29/16	Mon 7/4/16
35	Install Aluminum Fence	5 days	Tue 7/5/16	Mon 7/11/16
36	Landscape	3 days	Tue 7/5/16	Thu 7/7/16
37	Demobilize/Restoration	3 days	Fri 7/8/16	Tue 7/12/16

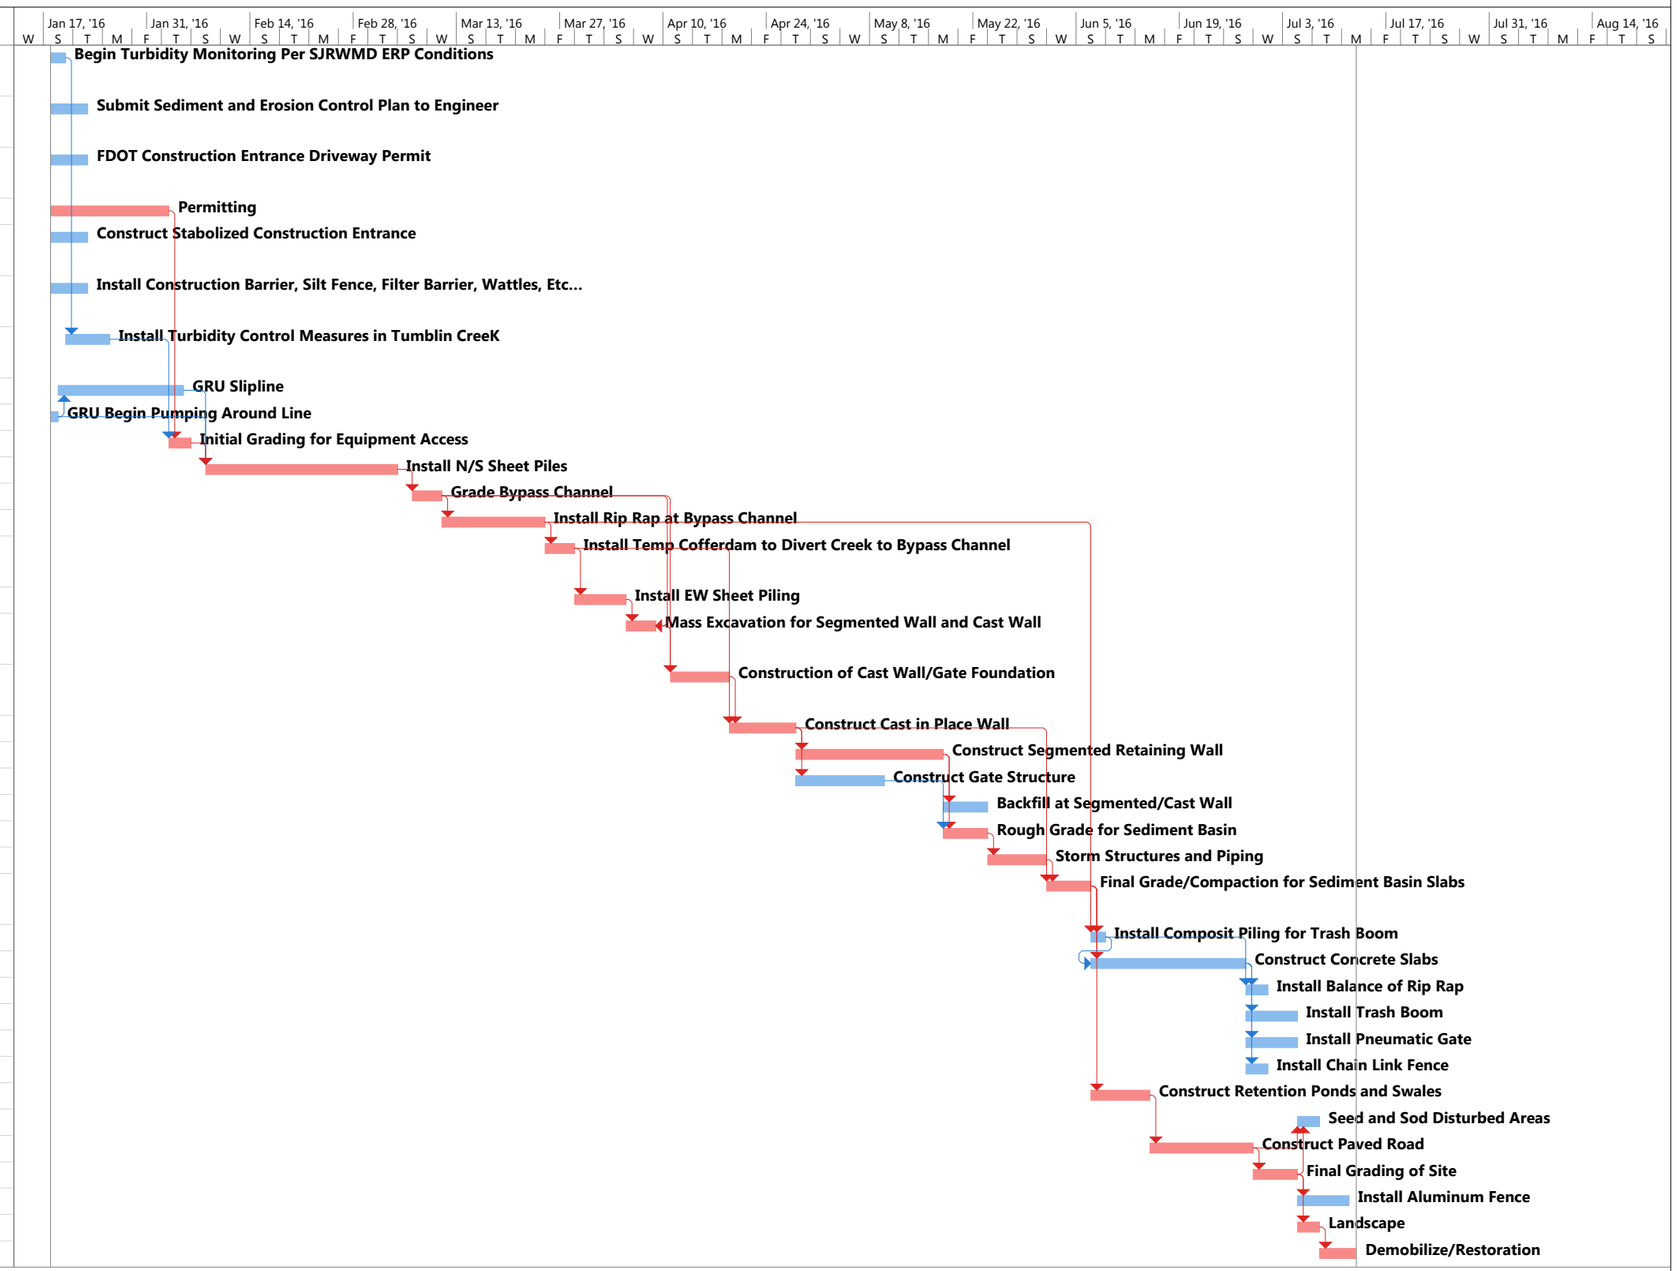

Project: Tumblin Creek Trash Tr
Date: Fri 11/20/15

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Critical Split	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline		Progress	
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Critical		Manual Progress	
